

Abu Dhabi National Oil Company (ADNOC) Group Digital Initiative

ADNOC L&S ERP Transformation

أدنوك
ADNOC

Contents

1 Executive Summary 4
1.1 Context and Objectives 4
1.2 General scope of services and timeline 5
1.3 Guiding principles 6
2 Scope of work 7
2.1 SAP Implementation – Enterprise structure 7
2.2 SAP Implementation - Processes 7
2.3 SAP implementation – Application and integration 17
2.4 SAP implementation – RICEFWS 20
2.5 SAP implementation – Infrastructure & Accesses 22
2.6 SAP Implementation – Data Cleansing 22
2.7 SAP Implementation – Data Migration 23
2.8 SAP Implementation – Testing 24
2.9 SAP Implementation - Application Security (Roles and Authorizations Management) 25
2.10 SAP Implementation – Change management 25
2.11 SAP Implementation – HyperCare 26
2.12 GBS TOM Design 27
2.13 Infrastructure design – Infra & Cybersecurity current state assessment 28
2.14 Infrastructure design – Non-ERP Application Hosting Strategy 30
2.15 Infrastructure design – ERP Cybersecurity Assessment 31
2.16 Additional Enhancements & Integrations 34
3 AI-Enabled Transformation 34
3.1 Scope and expectations 34
3.2 Core capabilities requirements 35
3.2 Delivery Model requirements 36
3.4 Tooling Requirements 36
3.5 AI Deliverables (build Layer) 36
3.6 ADNOC AI Reference Architecture 37
4 Project methodology 38
4.1 Project plan 38
4.2 RACI 38
4.3 Deliverables 40
4.4 Program organization 42
4.5 Program governance 43
4.6 Collaboration with 3rd Parties 44

4.7 Standards and Guidelines of OneERP 45
4.8 Project Location 50
5 Upgrade Activities 51
6 ZMI & Navig8 Reference Architecture 51
7 RFP instruction 51
5.1 Expected content of the response 51
5.2 Evaluation Approach 51

1 Executive Summary

1.1 Context and Objectives


ADNOC Logistics & Services [L&S] is the region's largest shipping and integrated logistics company and a global energy maritime logistics leader with a world-class asset base.

ADNOC L&S was established in 2016 through the integration of several ADNOC entities operating in integrated logistics, shipping, and marine services, with its heritage tracing back to the formation of the Abu Dhabi National Tanker Company in 1975.

L&S has developed its business through a combination of organic growth, fleet expansion, acquisitions, joint ventures, and innovative integrated offerings, both to support ADNOC's wider growth ambitions and service a growing portfolio of global customers and markets. Most recently L&S has completed the acquisitions of Navig8 and ZMI, and through those, L&S group is now a global, 24/7 shipping and logistics group with high operational complexity and performance expectations. L&S group operates in the following key business segments

- Commercial shipping
- Ship management
- Integrated logistics, including both offshore and onshore logistics
- Marine operations, including ports operations and oil spill responses

Below a simplified representation of L&S group business segments

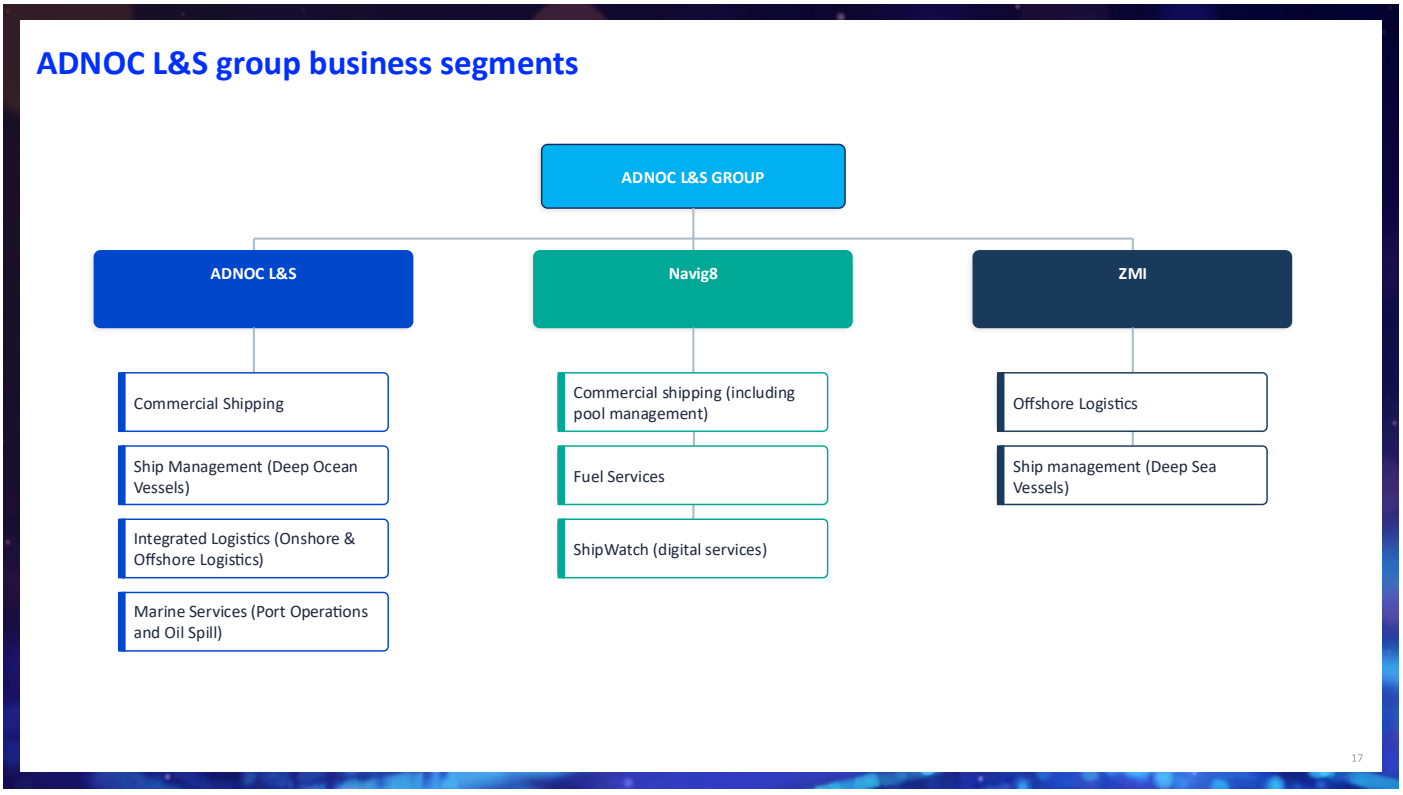

ADNOC L&S is undergoing a transformation to integrate its core operations and subsidiaries into a more unified, scalable, and efficient operating model. Today, L&S and its subsidiaries operate with a fragmented landscape of processes and systems both across front end and enterprise operations, limiting visibility, increasing manual effort, and constraining the ability to leverage group-wide synergies.

As part of this transformation, L&S aims to incorporate the whole group into a unified marine and shipping SAP template, within ADNOC OneERP instance, and explore the design and establish a Global Business Services (GBS) model for Finance and Procurement. This initiative will enable standardization of processes, improve data consistency, strengthen governance, and support future growth across the group.


The objectives of this engagement are to:

- Design and implement a standardized ERP template across L&S and its subsidiaries to harmonize processes to industry best practices
- Ensure the integration of the ERP with ADNOC BW layer and with One BPC for reporting with the rest of the group
- Enable a single source of truth for financial and operational data across the organization
- Enhance operational control, and decision-making capabilities across L&S and subsidiaries
- Ensure seamless integration of the ERP with the ADNOC Data Hub
- Explore the design and establish a GBS operating model to centralize and streamline Finance and Procurement activities to optimize process efficiency and cost

1.2 General scope of services and timeline

The scope of this transformation shall cover the design, implementation, and rollout of a unified ERP platform across ADNOC L&S and its subsidiaries, together with the design of a Global Business Services (GBS) model for Finance and Procurement.

The ERP scope shall include the onboarding of subsidiaries into the OneERP ADNOC instance and the harmonization of core processes including Finance (including controlling, funds management, treasury, …), Procurement, Inventory Management, Human Capital Management, Sales, and Plant Maintenance. The transformation shall adopt a fit-to-gap approach based on the ADNOC ERP template, leveraging the existing template to accelerate deployment while allowing for localization as per L&S and subsidiaries requirements. The scope shall also include integration with key business solution supporting front-end shipping and marine activities (e.g., IMOS by Veson, AMOS, …). Below a high-level representation of the current application landscape and the integration flows between the business solutions and the ERPs

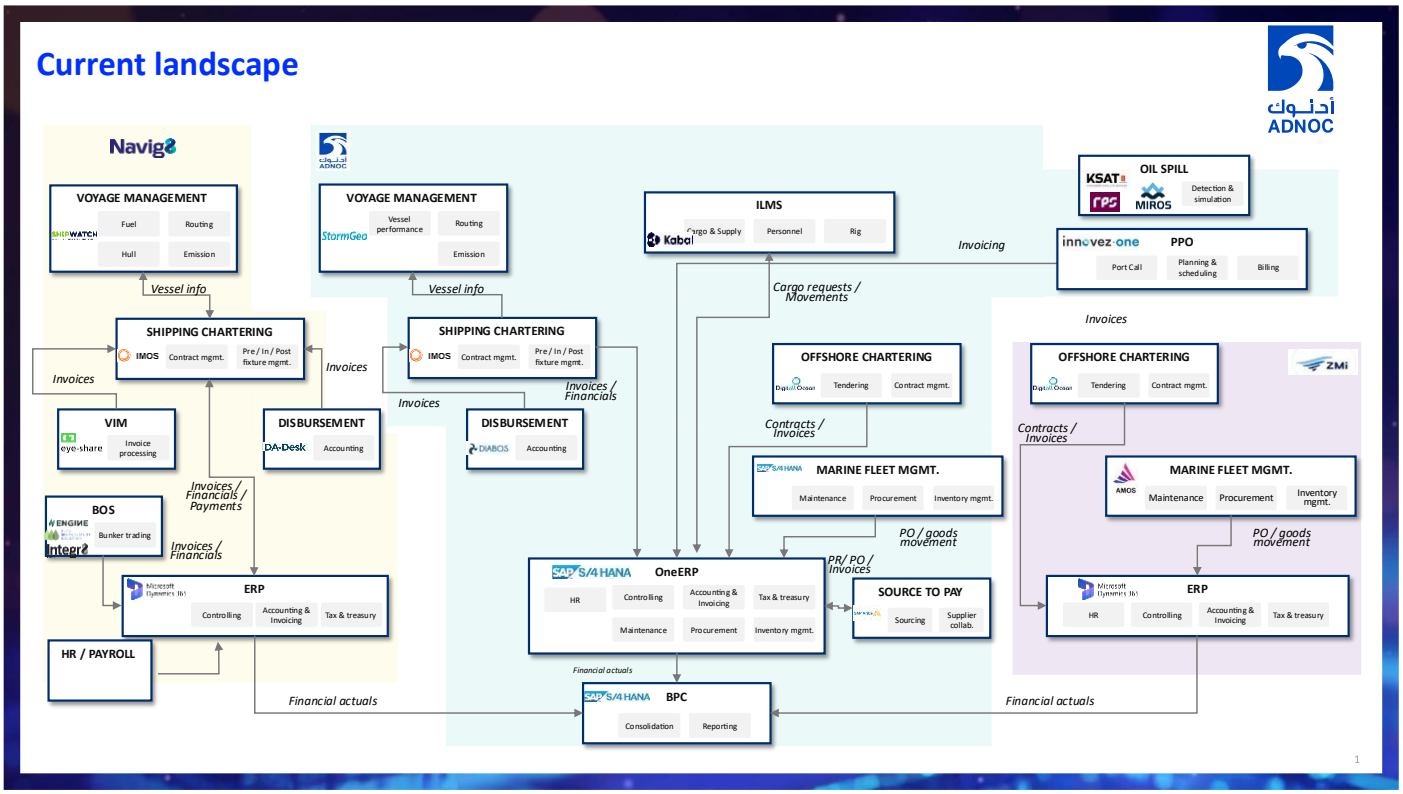

In parallel, the GBS scope shall include the design of a centralized service delivery model primarily covering transactional Finance and Procurement processes, supported by defined governance frameworks, service management structures, and performance management mechanisms.

ADNOC L&S plans to initiate the design phase by the end of Q2 2026, complete the design of both the ERP solution and the GBS model by the end of 2026, and complete the implementation between Q3 and Q4 through a phased rollout across entities, starting with L&S and followed by its subsidiaries.

1.3 Guiding principles

The ERP and GBS design and implementation shall adhere to the following guiding principles:

- **Fit-to-Gap Approach** - Adopt a fit-to-gap methodology based on the ADNOC ERP template, starting from the existing template to accelerate deployment while creating variants and changes based on the business nuances
- **Harmonization across L&S group** - Standardize core enterprise processes across L&S and subsidiaries, leveraging best practices from subsidiaries
- **Lean ERP setup for core enterprise Functions** - Position ERP as the system of record for enterprise processes (Month-end closure, Payments, Corporate procurement, …etc.), while maintaining specialized operational systems (e.g., IMOS for commercial shipping and accounting, AMOS for ship management, DigitALL Ocean for commercial shipping of OSV, …) for core maritime activities, with clear segregation of responsibilities.
- **Scalability and Future Readiness** - Design the solution to support future business growth, including onboarding of new subsidiaries and changes in operating model
- **GBS operating model design** - Ensure the ERP design supports a Global Business Services model for Finance and Procurement that will be studied and designed during the engagement

2 Scope of work

ADNOC L&S is seeking a transformation partner to support this journey across three key workstreams: (i) SAP ERP implementation, (ii) Global Business Services (GBS) Target Operating Model design and (iii) Infrastructure design. The following sections provide further detail on the scope of services and support required from the bidder.

2.1 SAP Implementation – Enterprise structure

The bidder shall support the consolidation and setup of the enterprise data structure required to enable the OneERP model across ADNOC L&S and its subsidiaries.

The enterprise data setup shall cover the configuration of the core organizational and financial structures within SAP (including e.g. Company Codes, Plants, Business Units, Profit Centers, Cost Centers, Internal Orders, and Project/WBS structures, Sales organization, …). The bidder shall also support the setup in the system of a unified Chart of Accounts (aligned with ADNOC group standards) that will be provided by L&S and subsidiaries

In addition, the bidder shall define and implement master data governance processes, including data ownership, data maintenance procedures, approval workflows, and data quality controls, to ensure ongoing data accuracy, consistency, and integrity in the target environment.

While the final enterprise structure will be provided by L&S during the design phase, the below outlines the key components across the companies

COMPONENTS	**L&S** (including AW shipping)	**NAVIG8**	**ZMI**
# Legal entity	75	108	25
# Company codes	17	15	4
# employees	~2,000	~380 *(majority located across London, Singapore, and Mumbai)*	~600
# office location	1 UAE	11 UK, Singapore, USA, India, Brazil, UAE, Greece, Norway, Japan, China, Germany	5 UAE, KSA, Qatar
# plants	60 (approx. 50 vessel-related and 10 warehouse-related)	~10 (estimated plants for indirect purchases only, no warehouses)	~200 (3 warehouses, a couple of plant for indirect purchases only, rest is vessel-related plants)
# banks	4	12	10

** Legal entities are used for reporting purposes, while company codes represent the operational entities that must be configured in the system*

*** The implementation will be carried out across multiple locations, including Singapore, London, Mumbai, Abu Dhabi, and Dubai*

2.2 SAP Implementation - Processes

This section provides an overview of the business processes to be covered by the OneERP template (including SAP and related applications such as SAP Ariba and SuccessFactors) and that will require harmonization across ADNOC L&S and its subsidiaries.

As outlined above, the starting point for process design is the ADNOC OneERP template, with the expectation that a **fit-to-gap approach** will be applied. This approach prioritizes the adoption of standard processes while allowing targeted adjustments where required to meet business needs

The tables below outline the list of processes and indicate the expected level of redesign compared to the current OneERP template, using the following scale:

1. Adopt: The process is expected to be adopted as per the current OneERP template with no changes in L&S and to be rolled out with no changes to the subsidiaries
2. Enhance: The process requires a moderate level of review and adjustment (typically affecting less than 20% of the process). "Enhance" should not be interpreted as a RICEFW development or enhancement effort; rather, it refers to process refinements, configuration changes, or minor adjustments
3. Redesign: Process will be significantly rethought and redesigned, potentially including integration with new applications

It should be noted that when the same classification is applied across all three entities (e.g., all are tagged as “Redesign”), this indicates that a transformation effort is required to establish a common, standardized process across the group. Conversely, when the classification differs between entities, this reflects inherent differences in business requirements, and the process is expected to remain localized rather than fully standardized.

This assessment is preliminary and will be validated and refined during the design phase

Finance

Within the Finance domain, transactional processes are expected to be redesigned, considering the operationally intensive nature of the subsidiaries. In addition, the process landscape will be significantly impacted by: i) the exit from ADNOC Shared Services, ii) the establishment of a group-wide GBS organization across L&S, and iii) the principle of relocating operational business activities from SAP into specialized business solutions. This will require a substantial review of the ERP integration landscape, including systems such as IMOS commercial shipping activities of the deep ocean fleet, DigitALL Ocean for OSV commercial activities, and the bunker trading platform BOS.

The guiding principle for Finance will be to leverage best practices from Navig8 and ZMI to inform and redesign standardized processes at group level.

In addition, the Finance scope shall include the setup of the revised Chart of Accounts and new Cost Center and Profit Center hierarchy to support the new operating model and reporting requirements of L&S and its subsidiaries.

Note: Payments for ADNOC L&S will follow the existing setup (using the inhouse cash (AGT) and local bank payment) whereas subsidiary’s (Navig8 & ZMI) payment would be through their operating bank accounts which should include H2H connectivity for payments and bank reconciliation

STREAM	PROCESS	L&S	NAVIG8	ZMI
Accounts Payable	AP - AR Netting	Adopt	Adopt	Adopt
Accounts Payable	Commitment (PO) Invoices	Adopt	Adopt	Adopt
Accounts Payable	Invoice Reversal	Adopt	Adopt	Adopt
Accounts Payable	Manage Petty Cash payments and replenishment	Adopt	Adopt	Adopt
Accounts Payable	Manage Retention	Adopt	Adopt	Adopt
Accounts Payable	Manage Vendor Master Data	Redesign	Redesign	Redesign
Accounts Payable	Manage Vendor Payment	Enhance	Enhance	Enhance
Accounts Payable	Non-Commitment - Miscellaneous Invoices	Redesign	Redesign	Redesign
Accounts Payable	Pay on Receipt Auto Invoice ERS	Adopt	Adopt	Adopt
Accounts Payable	Vendor Correspondence	Adopt	Adopt	Adopt
Accounts Payable	Vendor Down Payment PO and Non-PO based	Adopt	Adopt	Adopt

STREAM	PROCESS	L&S	NAVIG8	ZMI
Accounts Receivable	Bad Debts Accounting	Adopt	Adopt	Adopt
Accounts Receivable	Credit Management	Redesign	Redesign	Redesign
Accounts Receivable	Customer Correspondence	Adopt	Adopt	Adopt
Accounts Receivable	Customer Down Payments	Adopt	Adopt	Adopt
Accounts Receivable	Customer Invoices and Credit Memos	Redesign	Redesign	Redesign
Accounts Receivable	Dunning Processing	Adopt	Adopt	Adopt
Accounts Receivable	Incoming Payments	Adopt	Adopt	Adopt
Accounts Receivable	Interests calculation	Enhance	Enhance	Enhance
Accounts Receivable	Manage Customer Master Data	Redesign	Redesign	Redesign
Asset Accounting	Asset Acquisition process with project WBS	Adopt	Adopt	Adopt
Asset Accounting	Asset capitalization through Work order (Internal Activity)	Adopt	Adopt	Adopt
Asset Accounting	Asset Depreciation	Adopt	Adopt	Adopt
Asset Accounting	Asset Impairment/ Revaluation	Adopt	Adopt	Adopt
Asset Accounting	Asset Intercompany Transfer	Adopt	Adopt	Adopt
Asset Accounting	Asset Intracompany Transfer	Adopt	Adopt	Adopt
Asset Accounting	Asset Master Data creation and approval process	Adopt	Adopt	Adopt
Asset Accounting	Asset Physical Count	Adopt	Adopt	Adopt
Asset Accounting	Asset Retirement	Adopt	Adopt	Adopt
Asset Accounting	Asset Transfer Change in Location	Adopt	Adopt	Adopt
Asset Accounting	Asset Scrapping / value update	Enhance	Enhance	Enhance
Bank Communication Management	Bank Communication Management (Payment release as per DOA)	Enhance	Enhance	Enhance
Bank Communication Management	Bank Master Data Management	Adopt	Adopt	Adopt
Bank Communication Management	Incoming Acknowledgement file	Enhance	Enhance	Enhance
Bank Communication Management	Incoming Bank Statement Processing - Electronic	Enhance	Enhance	Enhance
Bank Communication Management	Outgoing Payments - Payroll	Enhance	N/A	Enhance
Bank Communication Management	Outgoing Vendor Treasury Payments	Enhance	Enhance	Enhance
Bank Communication Management	Payment by Cheques	Enhance	Enhance	Enhance
SAC / BPC	Revenue Planning	Enhance	Enhance	Enhance
SAC / BPC	CAPEX and OPEX Planning	Enhance	Enhance	Enhance
SAC / BPC	Financial Planning incl Cash Flow	Enhance	Enhance	Enhance
SAC / BPC	Manpower Planning for Vessel Employees (MPD)	Enhance	Enhance	Enhance
SAC / BPC	What If scenarios	Enhance	Enhance	Enhance
SAC / BPC	Budget, Rolling Forecast, Forecast/Outlook, Business Plan	Enhance	Enhance	Enhance
SAC / BPC	Consolidation	Enhance	Enhance	Enhance
SAC / BPC	Profitability Planning	Enhance	Enhance	Enhance
Funds Management	Budget Availability Check	Enhance	Enhance	Enhance
Funds Management	Budget Execution and Distribution	Enhance	Enhance	Enhance
Funds Management	Budget vs Actual Reporting	Adopt	Adopt	Adopt
Funds Management	Commitment Item Master Data Maintenance	Enhance	Enhance	Enhance
Funds Management	Fund Center Master Data Maintenance	Adopt	Adopt	Adopt
Funds Management	OPEX budget management (Initiation and Approval)	Enhance	Enhance	Enhance
Funds Management	Derivation Strategy Enhancement to include Material Group	Enhance	Enhance	Enhance
General Ledger	Payment Amortization (using custom program)	Adopt	Adopt	Adopt

STREAM	PROCESS	L&S	NAVIG8	ZMI
General Ledger	AP-AR Cross Company Code Transactions	Enhance	Enhance	Enhance
General Ledger	Document Change and Reversal	Adopt	Adopt	Adopt
General Ledger	Financial Closing Cockpit	Adopt	Adopt	Adopt
General Ledger	Financial Statement Version	Adopt	Adopt	Adopt
General Ledger	General Ledger Journal Posting	Adopt	Adopt	Adopt
General Ledger	GL Cross Company and Intercompany Reconciliation	Enhance	Enhance	Enhance
General Ledger	GL Foreign Currency Maintenance and Valuation	Adopt	Adopt	Adopt
General Ledger	GL Recurring Entries and Accruals	Adopt	Adopt	Adopt
General Ledger	GL Year-End Closing	Adopt	Adopt	Adopt
General Ledger	GR/IR Analysis	Adopt	Adopt	Adopt
General Ledger	Manage GL Master Data and Account Extension	Enhance	Enhance	Enhance
General Ledger	Manage Manual & Automatic Clearing	Adopt	Adopt	Adopt
General Ledger	Open & Close FI Period	Adopt	Adopt	Adopt
General Ledger	Reclassification AR and AP	Adopt	Adopt	Adopt
Overheads Management	Activity Type Master Data	Adopt	Adopt	Adopt
Overheads Management	Actual Overheads Allocation	Adopt	Adopt	Adopt
Overheads Management	Cost Center Activity Output Planning	Adopt	Adopt	Adopt
Overheads Management	Cost Center Master data, Hierarchy & Cost Center Groups	Adopt	Adopt	Adopt
Overheads Management	Cost Center Planning	Redesign	Redesign	Redesign
Overheads Management	Cost Element Groups	Adopt	Adopt	Adopt
Overheads Management	Internal Order Master Data	Enhance	Enhance	Enhance
Overheads Management	Overheads Management Reporting	Adopt	Adopt	Adopt
Overheads Management	Plan Overheads Allocation	Enhance	Enhance	Enhance
Overheads Management	Profit Center Master data, Hierarchy & Profit Center Groups	Adopt	Adopt	Adopt
Overheads Management	Statistical Key Figure Master Data	Adopt	Adopt	Adopt
Overheads Management	Statistical Key Figure Planning	Adopt	Adopt	Adopt
Overheads Management	Cost Center Budget Control	Redesign	Redesign	Redesign
General Ledger	Interface from Satellite Systems for GL Accruals and or Reversals	Enhance	Enhance	Enhance
Product Costing	Activity Plan Pricing	Adopt	Adopt	Adopt
Product Costing	Define Cost Component Structure	Adopt	Adopt	Adopt
Product Costing	Make to Order	Adopt	Adopt	Adopt
Product Costing	Period-End Processing	Adopt	Adopt	Adopt
Product Costing	Product Cost Estimate	Adopt	Adopt	Adopt
Profitability Analysis	Profitability Actual Data	Adopt	Adopt	Adopt
Profitability Analysis	Profitability Planning	Adopt	Adopt	Adopt
Profitability Analysis	Profitability Reports	Adopt	Adopt	Adopt
Project Systems	AFE Request Initiation and Approval	Enhance	Enhance	Enhance
Project Systems	CAPEX budget management (Initiation and Approval)	Enhance	Enhance	Enhance
Project Systems	Period-end and Year-end Closing	Adopt	Adopt	Adopt
Project Systems	Project Actuals Cost Management	Adopt	Adopt	Adopt
Project Systems	Project Budgeting	Adopt	Adopt	Adopt
Project Systems	Project Close	Adopt	Adopt	Adopt
Project Systems	Project Planning	Adopt	Adopt	Adopt
Project Systems	Project Structure	Adopt	Adopt	Adopt
Project Systems	Project Systems Reporting	Adopt	Adopt	Adopt
Project Systems	Project Systems Revenue Projects and Settlement	Adopt	Adopt	Adopt

STREAM	PROCESS	L&S	NAVIG8	ZMI
Project Systems	Settlement Rule Individual and Mass Settlement Rule upload	Adopt	Adopt	Adopt
Project Systems	Project Systems CAPEX, OPEX, Recharges – Cost and Settlement	Adopt	Adopt	Adopt
Real Estate Management	Cost Recovery	Adopt	Adopt	Adopt
Real Estate Management	Lease Management (Amortization Run)	Enhance	Enhance	Enhance
Real Estate Management	Lease Management (Balance Sheet Valuation Posting)	Enhance	Enhance	Enhance
Real Estate Management	Lease Management (One Time Posting) & (Periodic Posting) and (Reversal Posting)	Adopt	Adopt	Adopt
Real Estate Management	Lease Management (Sales based rent settlement)	Adopt	Adopt	Adopt
Real Estate Management	Real Estate Master Data	Adopt	Adopt	Adopt
Real Estate Management	Real Estate Search	Adopt	Adopt	Adopt
Real Estate Management	Rent Calculation Method	Adopt	Adopt	Adopt
Real Estate Management	Space Management	Adopt	Adopt	Adopt
Real Estate Management	Long Term Lease IFRS enablement	Enhance	Enhance	Enhance
Taxes	VAT - Customer Down payments	Redesign	Redesign	Redesign
Taxes	VAT - Customer Invoice Processing	Redesign	Redesign	Redesign
Taxes	VAT - VAT Reporting-Entity Level	Redesign	Redesign	Redesign
Taxes	VAT - VAT Reporting-Group Level	Redesign	Redesign	Redesign
Taxes	VAT - Vendor Down Payment and Retention Settlement	Redesign	Redesign	Redesign
Taxes	VAT - Vendor Invoice Processing	Redesign	Redesign	Redesign
Taxes	VAT specific Master Data	Enhance	Enhance	Enhance
Taxes	With holding Tax or any other tax in line with the country regulations	Redesign	Redesign	Redesign
Treasury Management	Bank Guarantee	Adopt	Adopt	Adopt
Treasury Management	Cash Management Reporting	Enhance	Enhance	Enhance
Treasury Management	Currency Trade (Buy & Sell)	Adopt	Adopt	Adopt
Treasury Management	Facility Process	Enhance	Enhance	Enhance
Treasury Management	Fixed Term Deposit	Adopt	Adopt	Adopt
Treasury Management	Forex Swap Process	Adopt	Adopt	Adopt
Treasury Management	Intercompany Loan Process	Enhance	Enhance	Enhance
Treasury Management	Letter of Credit	Adopt	Adopt	Adopt
Treasury Management	Loan Drawdown Process	Enhance	Enhance	Enhance
Treasury Management	Exchange Rate management	Redesign	Redesign	Redesign
Treasury Management	Interbank / Intra Bank Transfer (Intercompany/Intra company)	Redesign	Redesign	Redesign
Treasury Management	Hybrid Capital management	Enhance	Enhance	Enhance
Treasury Management	Direct and Indirect Cashflow reporting	Redesign	Redesign	Redesign

Procurement

Within the Procurement domain, processes are also expected to be redesigned, driven by the principle of relocating operational activities into specialized business solutions. This is particularly relevant for ship management procurement processes, where the bidder will be required to review the integration model between the ship management solution and SAP, and work with the L&S group to define the target allocation of processes, responsibilities, and data flows across the two platforms.

In addition, the procurement process landscape will be impacted by: i) the exit from ADNOC Shared Services, and ii) the establishment of a dedicated GBS organization within L&S.

Indirect procurement processes are expected to largely align with the current OneERP template, with targeted enhancements to sourcing workflows across SAP Ariba, TBMS and Vendor portal to improve the overall efficiency.

STREAM	PROCESS	L&S	NAVIG8	ZMI
Embedded Analytics	Key Performance Indicator Analysis	Adopt	Adopt	Adopt
Embedded Analytics	Operational Reporting	Adopt	Adopt	Adopt
Execute Transactional Sourcing (Operational)	Manage invoices / Credit memos	Enhance	Enhance	Enhance
Execute Transactional Sourcing (Operational)	Manage quality in procurement	Adopt	Adopt	Adopt
Execute Transactional Sourcing (Operational)	Manage receipts (GRN & SES) and confirmation	Adopt	Adopt	Adopt
Execute Transactional Sourcing (Operational)	Process purchase orders	Enhance	Enhance	Enhance
Execute Transactional Sourcing (Operational)	Process Purchase Requisitions	Enhance	Enhance	Enhance
Inventory Management	MRP planning	Enhance	Enhance	Enhance
Inventory Management	Inventory Management Report	Redesign	Redesign	Redesign
Inventory Management	Manage Goods Issues	Adopt	Adopt	Adopt
Inventory Management	Manage Goods Receipts	Adopt	Adopt	Adopt
Inventory Management	Manage Inventory Valuation	Adopt	Adopt	Adopt
Inventory Management	Manage Stock Transport Orders and Transfers	Adopt	Adopt	Adopt
Inventory Management	Master data	Adopt	Adopt	Adopt
Inventory Management	Physical Inventory Count	Adopt	Adopt	Adopt
Inventory Management	Manage return	Enhance	Enhance	Enhance
Inventory Management	Manage intercompany Sale / Loan process	Adopt	Adopt	Adopt
Manage Logistics	Expediting Log	Enhance	N/A	Enhance
Manage Logistics	Manage Logistic Services with 3PL	Adopt	N/A	Adopt
Manage Logistics	Notifications	Adopt	N/A	Adopt
Manage Logistics	Settlement of logistic service cost with 3PL	Adopt	N/A	Adopt
Manage MRO Stores and Inventory	Define MRO Storage and Inventory Strategy	Adopt	N/A	Adopt
Manage MRO Stores and Inventory	Manage MRO Stores	Adopt	N/A	Adopt
Perform Strategic Sourcing	Conduct negotiations	Redesign	Redesign	Redesign
Perform Strategic Sourcing	Conduct RFP Auctions	Redesign	Redesign	Redesign
Perform Strategic Sourcing	Manage master data and content	Adopt	Adopt	Adopt
Perform Strategic Sourcing	Managing Catalog Content	Adopt	Adopt	Adopt
Perform Strategic Sourcing	Screen and Prequalify Potential Suppliers	Redesign	Redesign	Redesign
Perform Strategic Sourcing	Shape and Negotiate Supply Contracts	Redesign	Redesign	Redesign
Perform Strategic Sourcing	Spend and Opportunity Analysis	Redesign	Redesign	Redesign
Perform Strategic Sourcing	Supplier Management	Redesign	Redesign	Redesign
Process RFx	Approve or Reject Bid	Enhance	Enhance	Enhance
Process RFx	Approve Publication of Bid Invitation	Enhance	Enhance	Enhance
Process RFx	Change Bid Invitation	Enhance	Enhance	Enhance
Process RFx	Complete and Save Bid Invitation	Enhance	Enhance	Enhance
Process RFx	Create and Submit Bid	Enhance	Enhance	Enhance
Process RFx	Create Bid Invitation	Enhance	Enhance	Enhance
Process RFx	Create Collaborative bid invitation	Enhance	Enhance	Enhance
Process RFx	Evaluate Bid	Enhance	Enhance	Enhance
Process RFx	Manage 2 Envelope Bidding	Enhance	Enhance	Enhance
Process RFx	Process Workload Reassignment	Enhance	Enhance	Enhance
Process RFx	Processing Collaborative Bid Events Using cFolders	Enhance	Enhance	Enhance
Process RFx	Publish Bid Invitation	Enhance	Enhance	Enhance
Process RFx	Publish Collaborative Bid Invitation	Enhance	Enhance	Enhance
Process RFx	Return to Vendor	Enhance	Enhance	Enhance

STREAM	PROCESS	L&S	NAVIG8	ZMI
Process RFx	Update Collaborative Documents	Enhance	Enhance	Enhance
Process RFx	Upload Bid Invitation from File	Enhance	Enhance	Enhance
Supplier Collaboration	Manage Supplier onboarding	Enhance	Enhance	Enhance
Supplier Collaboration	Manage Supplier Performance	Enhance	Enhance	Enhance
Supplier Collaboration	Manage Supply Contracts	Enhance	Enhance	Enhance
Supplier Collaboration enablement	Accept - Acknowledge PO Response	Adopt	Adopt	Adopt
Supplier Collaboration enablement	Change Purchase Order	Adopt	Adopt	Adopt
Supplier Collaboration enablement	Check open invoices	Adopt	Adopt	Adopt
Supplier Collaboration enablement	Create ASNs	Adopt	Adopt	Adopt
Supplier Collaboration enablement	Create Entry Sheet	Adopt	Adopt	Adopt
Supplier Collaboration enablement	Create invoice	Adopt	Adopt	Adopt
Supplier Collaboration enablement	Create PO Response	Adopt	Adopt	Adopt
Supplier Collaboration enablement	View ASNs	Adopt	Adopt	Adopt
Supplier Collaboration enablement	View Entry Sheet	Adopt	Adopt	Adopt
Supplier Collaboration enablement	View individual invoices	Adopt	Adopt	Adopt
Supplier Collaboration enablement	View invoices per purchase order	Adopt	Adopt	Adopt
Supplier Collaboration enablement	View invoices per vendor	Adopt	Adopt	Adopt
Supplier Collaboration enablement	View open deliveries	Adopt	Adopt	Adopt
Tender Board Management	Award Submission	Redesign	Redesign	Redesign
Tender Board Management	Bidders list Submission	Redesign	Redesign	Redesign
Tracking and Traceability	Batch Management & Serial number	Adopt	N/A	Adopt
Warehouse Management	Cross Module Integration for WM	Adopt	N/A	Adopt
Warehouse Management	Inventory Count in Warehouse Management	Adopt	N/A	Adopt
Warehouse Management	Optimize Warehouse Operations	Adopt	N/A	Adopt
Warehouse Management	Transfer Material in Warehouse Management	Adopt	N/A	Adopt
Warehouse Management	WM Inbound processing and Receipt Confirmation	Adopt	N/A	Adopt
Warehouse Management	WM Organization hierarchy and master data	Adopt	N/A	Adopt
Warehouse Management	WM Outbound Processing	Adopt	N/A	Adopt
Contract Management	Creation/Modification of contract	Enhance	Enhance	Enhance
Contract Management	Contract Term and Condition	Adopt	Adopt	Adopt
Contract Management	Contract Administration	Adopt	Adopt	Adopt
Contract Management	Consumption Control	Adopt	Adopt	Adopt
Contract Management	Contract Disputes/ Claims	Adopt	Adopt	Adopt
Contract Management	Master - sub agreement process	Adopt	Adopt	Adopt
Contract Management	Amendment Management	Adopt	Adopt	Adopt
Contract Management	Renewal Management	Adopt	Adopt	Adopt
Contract Management	Performance Management	Adopt	Adopt	Adopt
Contract Management	Contract closure	Adopt	Adopt	Adopt


HCM

Within the HCM domain, processes are expected to adopt the current OneERP template for L&S while the subsidiaries will inherit L&S system but will define the required localization to the available process templates.

For subsidiaries, the scope of deployment will be limited to core HCM processes (e.g. setup of organization structure, grades, …), onboarding and offboarding, recruitment, payroll, and time management. Advanced HCM functionalities—such as competency management, learning development and succession planning —are not expected to be deployed for these entities.

For Navig8 specifically, the payroll process is executed outside of the ERP and it will only need to be integrated with SAP for financial recording

This guidelines for the HR scope is to onboard the subsidiaries, maximizing the reuse of existing configurations with the required localization. It is not required to design L&S group wide HR processes or harmonize organizational structures.

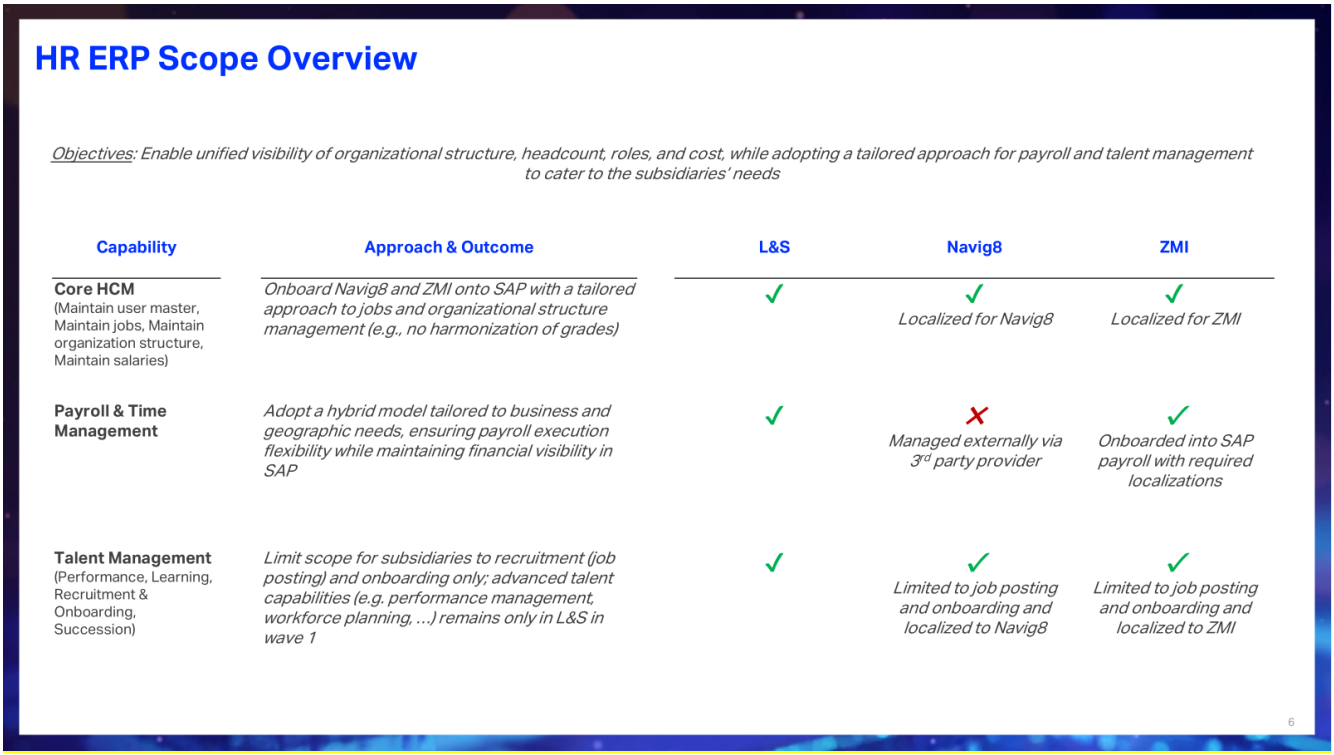

HR ERP Scope Overview

Objectives: Enable unified visibility of organizational structure, headcount, roles, and cost, while adopting a tailored approach for payroll and talent management to cater to the subsidiaries' needs

Capability	Approach & Outcome	L&S	Navig8	ZMI
Core HCM (Maintain user master, Maintain jobs, Maintain organization structure, Maintain salaries)	*Onboard Navig8 and ZMI onto SAP with a tailored approach to jobs and organizational structure management (e.g., no harmonization of grades)*	✓	✓ *Localized for Navig8*	✓ *Localized for ZMI*
Payroll & Time Management	*Adopt a hybrid model tailored to business and geographic needs, ensuring payroll execution flexibility while maintaining financial visibility in SAP*	✓	✗ *Managed externally via 3rd party provider*	✓ *Onboarded into SAP payroll with required localizations*
Talent Management (Performance, Learning, Recruitment & Onboarding, Succession)	*Limit scope for subsidiaries to recruitment (job posting) and onboarding only; advanced talent capabilities (e.g. performance management, workforce planning, …) remains only in L&S in wave 1*	✓	✓ *Limited to job posting and onboarding and localized to Navig8*	✓ *Limited to job posting and onboarding and localized to ZMI*

6

The solution will run on a shared instance with strict role-based access controls ensuring full data isolation between companies, with L&S maintaining visibility across the group

STREAM	PROCESS	L&S	NAVIG8	ZMI
Competency Management and Career Development	Career development planning	Adopt	N/A	N/A
Competency Management and Career Development	Competency management	Adopt	N/A	N/A
Employee and Manager Self-Service	Manage employee relations disciplinary events	Adopt	N/A	N/A
Employee and Manager Self-Service	Manage employee relations grievances	Adopt	N/A	N/A
Learning Management and	Learning management and administration	Adopt	N/A	N/A

STREAM	PROCESS	L&S	NAVIG8	ZMI
Training administration				
Onboarding, Offboarding And Cross Boarding	Cross boarding	Adopt	Redesign	Redesign
Onboarding, Offboarding And Cross Boarding	Offboarding	Adopt	Redesign	Redesign
Onboarding, Offboarding And Cross Boarding	Onboarding	Adopt	Redesign	Redesign
Onboarding, Offboarding And Cross Boarding	Perform Rehire and complete all Hire Actions	Adopt	Redesign	Redesign
Organization Management	Maintain Jobs	Adopt	Redesign	Redesign
Organization Management	Maintain Organizational Units and Positions	Adopt	Redesign	Redesign
Payroll Management	Manage Loans and Advances	Adopt	N/A	Redesign
Payroll Management	Manage Payroll Data	Adopt	N/A	Redesign
Payroll Management	Perform post payroll activities	Adopt	N/A	Redesign
Payroll Management	Process agency contractor payroll	Adopt	N/A	Redesign
Payroll Management	Process off cycle payroll	Adopt	N/A	Redesign
Payroll Management	Process regular payroll	Adopt	N/A	Redesign
Performance and Goal Management	Performance and objective management	Adopt	N/A	N/A
Personal Administration (HR Data)	Complete final settlement	Adopt	N/A	Redesign
Personal Administration (HR Data)	Maintain HR Data	Adopt	Redesign	Redesign
Personal Administration (HR Data)	Maintain HR Data Duty Travel* (*Only rolling out existing HQ process and Platform)	Adopt	N/A	Redesign
Personal Administration (HR Data)	Maintain HR Data Employee Housing	Adopt	N/A	Redesign
Personal Administration (HR Data)	Maintain HR Data ESC-Change in Conditions	Adopt	N/A	Redesign
Personal Administration (HR Data)	Manage separation	Adopt	Redesign	Redesign
Recruitment Management	Recruitment management and approval	Adopt	Redesign	Redesign
Recruitment Management	Recruitment marketing	Adopt	Redesign	Redesign
Succession Planning	Succession planning	Adopt	N/A	N/A
Time Management	Manage time and maintain timekeeping	Adopt	N/A	Redesign
Time Management	Work Rotation Cyclic Schedule	Adopt	N/A	Redesign

Sales & Distribution

Within the Sales & Distribution domain, processes are expected to adopt the current OneERP template

Sales and distribution processes are primarily applicable to the Offshore and Ports business of L&S, where they are expected to continue largely as-is. Effort should focus on the review of the interfaces of systems like DigitALL Ocean that would trigger the billing to SAP. The applicability of these processes to ZMI's commercial offshore business shall be further assessed and validated during the design phase.

STREAM	PROCESS	L&S	NAVIG8	ZMI
Order to Cash	Invoice Customer	Adopt	N/A	Adopt

STREAM	PROCESS	L&S	NAVIG8	ZMI
Order to Cash	Maintain Customer Master Data	Adopt	N/A	Adopt
Order to Cash	Manage & Process Disputes / Deductions	Adopt	N/A	Adopt
Order to Cash	Manage Contracts & Quotations	Adopt	N/A	Adopt
Order to Cash	Manage Customer Requests & Inquiries	Adopt	N/A	Adopt
Order to Cash	Manage Sales Orders	Enhance	N/A	Adopt
Order to Cash	Intercompany company sales and purchase	Adopt	N/A	Adopt
Ports Operations	Charter Vessels	Enhance	N/A	N/A
Ports Operations	Collect Input for Vessel Requirements	Enhance	N/A	N/A
Ports Operations	Manage Loading and Unloading Operations	Adopt	N/A	N/A
Secondary Distribution Management	Maintain Secondary Distribution Master Data	Adopt	N/A	N/A
Secondary Distribution Management	Monitor secondary distribution performance	Adopt	N/A	N/A
Secondary Distribution Management	Schedule secondary distribution	Adopt	N/A	N/A
Secondary Distribution Management	Setup scheduling system	Adopt	N/A	N/A
Transportation Costing	Perform Ships Invoicing	Adopt	N/A	N/A

Maintenance

Within the Maintenance domain, the expectation is that the current OneERP processes will largely be adopted as-is for L&S.

A key change, aligned with the principle of relocating operational processes into specialized business solutions, is that vessel maintenance activities will be moved outside of SAP and managed within the dedicated ship management solution. As part of the scope, the bidder shall review and redesign the integration between ship management platform and SAP, with particular focus on financial and controlling processes such as cost accounting, accruals, liabilities, settlements, and capitalization logic.

The current ZMI high-level process and integration architecture should be leveraged as the baseline reference for defining the future interaction model between the ship management solution and SAP.

Maintenance processes within SAP are applicable only to L&S. ZMI is already managing maintenance activities through a dedicated ship management solution outside the ERP landscape, while Navig8 outsources technical vessel management activities to third parties

STREAM	PROCESS	L&S	NAVIG8	ZMI
Maintenance Reporting and KPIs	Maintenance Reporting and KPIs	Adopt	N/A	N/A
Multi Resource Scheduling	Multi Resource Scheduling	Adopt	N/A	N/A
Notification Processing	Activity Report	Adopt	N/A	N/A
Notification Processing	Breakdown Notification	Adopt	N/A	N/A
Notification Processing	Corrective Notification	Adopt	N/A	N/A
Order Processing	Breakdown	Adopt	N/A	N/A
Order Processing	Complete Order	Adopt	N/A	N/A
Order Processing	External Operations	Adopt	N/A	N/A
Order Processing	Non-Stock items	Adopt	N/A	N/A
Order Processing	Plan Order	Adopt	N/A	N/A
Order Processing	Release Order	Adopt	N/A	N/A
Order Processing	Schedule	Adopt	N/A	N/A
Order Processing	Time Confirmation	Adopt	N/A	N/A
PM Master Data	BOM	Adopt	N/A	N/A
PM Master Data	Equipment Master	Adopt	N/A	N/A
PM Master Data	Functional Location	Adopt	N/A	N/A
PM Master Data	Maintenance Plan	Adopt	N/A	N/A
PM Master Data	Measuring Point	Adopt	N/A	N/A

STREAM	PROCESS	L&S	NAVIG8	ZMI
PM Master Data	Task List	Adopt	N/A	N/A
PM Master Data	Work Center	Adopt	N/A	N/A
Preventive Maintenance	Counter base	Adopt	N/A	N/A
Preventive Maintenance	Deadline Monitoring	Adopt	N/A	N/A
Preventive Maintenance	Maintenance Item	Adopt	N/A	N/A
Preventive Maintenance	Measuring Documents	Adopt	N/A	N/A
Preventive Maintenance	Schedule Plan	Adopt	N/A	N/A
Preventive Maintenance	Time base	Adopt	N/A	N/A
Preventive Maintenance	Calibration	Adopt	N/A	N/A
Refurbishment Processing	GI Defective part	Adopt	N/A	N/A
Refurbishment Processing	GR refurbished	Adopt	N/A	N/A
Refurbishment Processing	Order Settlement	Adopt	N/A	N/A
Refurbishment Processing	Refurbishment Order Completion	Adopt	N/A	N/A
Refurbishment Processing	Valuation Types	Adopt	N/A	N/A
Shutdown Maintenance	Fleet Management	Adopt	N/A	N/A
Shutdown Maintenance	Pool Asset Management	Adopt	N/A	N/A
Shutdown Maintenance	Revisions	Adopt	N/A	N/A
Shutdown Maintenance	WBS	Adopt	N/A	N/A
Maintenance Reporting and KPIs	Maintenance Reporting and KPIs	Adopt	N/A	N/A

Others

Other modules within the OneERP template currently deployed in L&S (e.g. HSE, PPQM,…) are expected to be adopted as-is, with no changes required. These modules are applicable to L&S only and are not in scope for deployment across the subsidiaries

The design of business processes executed within specialized industry applications is out of scope for the bidder. The bidder shall only be responsible for the design or redesign of the integration model and process interaction between these applications and SAP. This includes, but is not limited to:

- Commercial shipping processes (e.g., pre-fixture, fixture, and post-fixture management) executed within IMOS and DigitALL Ocean
- Bunker trading processes executed within BOS
- Ship maintenance and crew management processes executed within the Ship Management Solution
- Offshore logistics management processes (e.g., cargo planning, vessel scheduling, and offshore operations coordination) executed within ILMS

2.3 SAP implementation – Application and integration

The table below outlines the key applications that will require integration with SAP. It also provides an indication of whether an integration currently exists and whether it is expected to be reviewed as part of the transformation.


Certain applications, such as ILMS and InnovezOne (port operations), are expected to remain largely unchanged, given that the underlying business processes will not be significantly impacted by the target ERP template.

The integration flows described in the table are indicative and will need to be reviewed by the bidder during the design phase in alignment with the new process design

Application	Application Description	Existing Integration with OneERP (Y/N)	Integration to be Reviewed (Y/N)	Scope of Integration (high-level)
IMOS	Commercial shipping and voyage management system used for large vessel fleet operations, including chartering, voyage accounting, and operational execution	Y	Y	IMOS->SAP: AP/AR invoices, Accruals & Other GL entries SAP->IMOS: Vendor/customer data
EyeShare	Invoice management solution for processing, validation, and approval of shipping vendor invoices	N	Y	EyeShare->SAP: AP invoices
AMOS / MaryAPP	Technical ship management system supporting planned maintenance, inventory, procurement, HSE , Crew management for vessel operations	N	Y	SAP->AMOS: Vendor and materials master data, budget, enterprise structure (e.g. plant, ..), PO AMOS->SAP: PO, Inventory, Goods movements, Time of offshore crew
DigitALLOcean	Operational system supporting Offshore Support Vessel (OSV) commercial activities (e.g. hiring and renting)	N	Y	DigitALL Ocean ->SAP: Contract, AP / AR invoices
Bunker operating system	BOS is the front office trading and ops system for all 70 bunker traders and operators. Used by traders to initiate credit and sanctions checks for deal approvals and to record deal details	N	Y	BOS->SAP: Invoicing data, financial postings SAP->BOS: Customer master data, enterprise structure
SAP Ariba	Procurement and sourcing platform supporting sourcing events, supplier collaboration, and contract management	Y	Y	
TBMS	Internal procurement governance and workflow system used for approval and control of sourcing activities	Y	N	
ILMS	System supporting OSV logistics planning, tracking, and coordination of materials and operations	Y	N	SAP->ILMS : SAP Contract, Material, Pricing ILMS -> SAP: Sales Order
Smart ports	Port and marine services platform supporting port operations, vessel services, and marine logistics coordination	Y	N	SmartPorts->SAP: Billing and invoice data
Payroll Navig8	Third-party payroll providers in the relevant locations across the globe for Navig8	N	Y	Payroll->SAP : Payroll journals It is expected to use one common interface to consume the financial posting from the external payroll providers for Navig8
SAC	Coud-based planning and analytics platform used for budgeting, forecasting, and financial consolidation.	Y	Y	
Success Factor	Cloud HCM suite managing the employee lifecycle — org structure, onboarding/offboarding, performance, recruitment, and time management.	Y	Y	Enhancement to the existing S4-SF interface for Org Objects to manage the adjustments for ZMI
FieldGlass	Cloud application for the onboarding and management of 3rd party man-power services	Y	N	


For reference, below is the current application architecture of the subsidiaries, which will eventually be migrated and integrated into ADNOC OneERP

Navig8

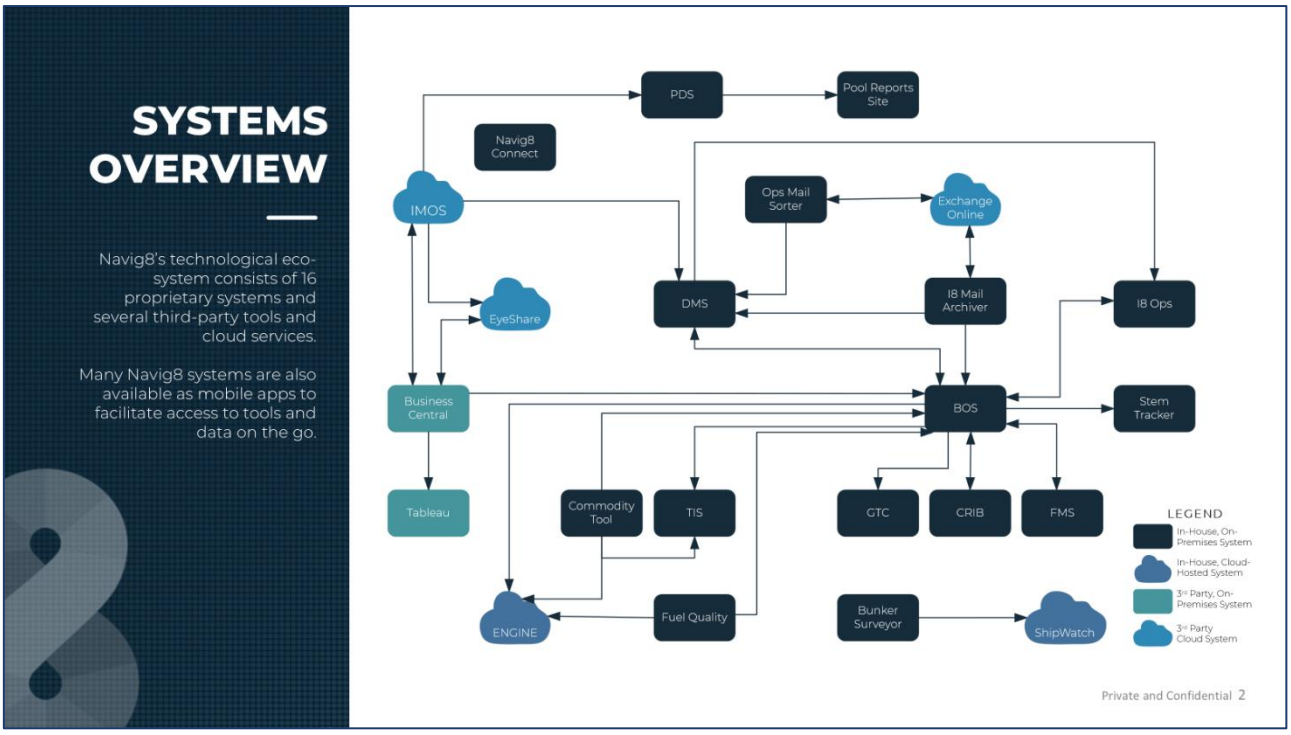



ZMI

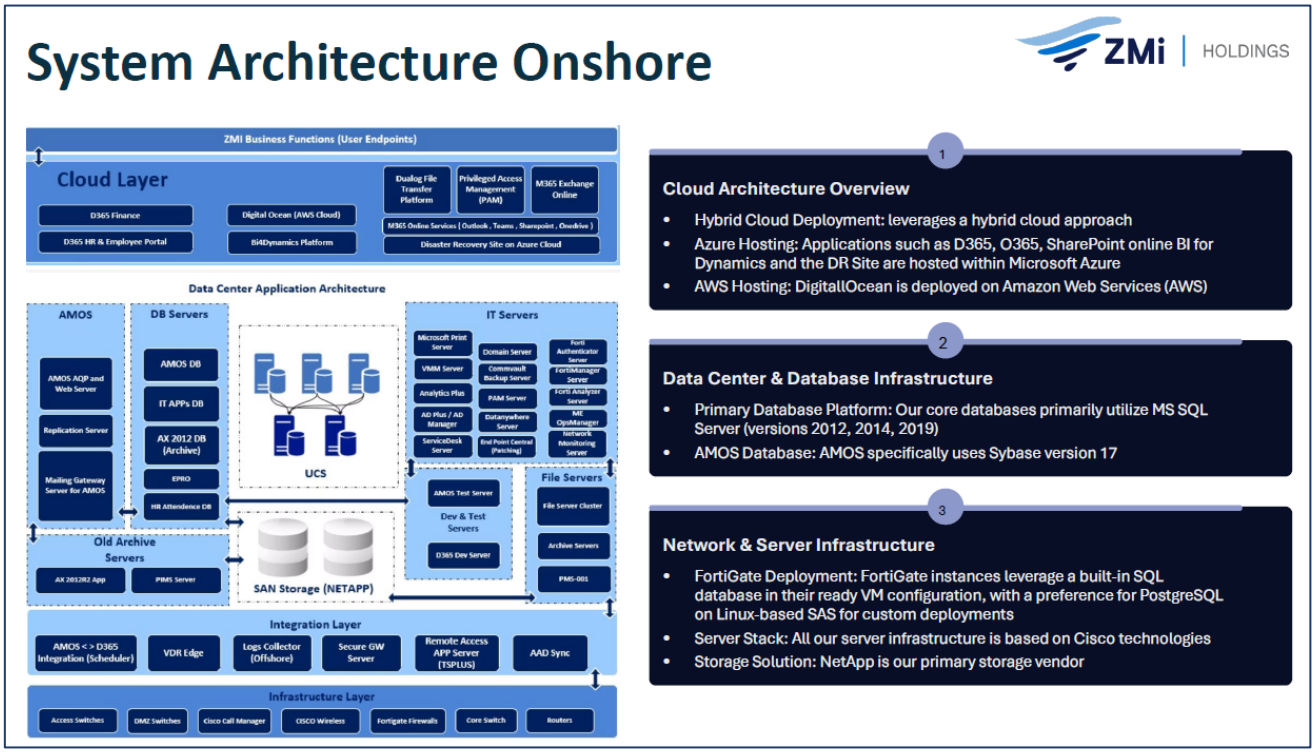

2.4 SAP implementation – RICEFWS

At this stage, the RICEFW objects identified should be considered as indicative placeholders for estimation purposes only. The final scope, design, and complexity of RICEFW objects will be validated and refined by the bidder during the Design Phase, based on detailed process design and key design decisions.

The table below provides an indicative distribution of RICEFW objects by category, including estimated complexity and examples of objects based on the preliminary assessment

OBJECT	ESTIMATED #	COMPLEXITY			SAMPLE PLACEHOLDER OBJECTS
		Low	Medium	High	
Reports (R)	30	10	14	6	AP ageing; AR ageing; Invoices status; PO status; Employee headcount; Financial settlements, ….
Interfaces (I)	30	7	15	8	IMOS->SAP invoices; IMOS->SAP accruals; IMOS->SAP GL entries; SAP->IMOS Vendor/Customer master; SAP->AMOS material master; SAP->AMOS vendor master; SAP->AMOS budget; AMOS->SAP purchase request; AMOS->SAP goods movement; Navig8 Payroll->SAP financial posting; ….
Conversions (C)	10	3	5	2	Vendor migration; Customer Migration; Open AP / AR & GL migration; Material Migration; Open stock migration; Asset Migration; PC/CC migration; …
Enhancements (E)	30	7	15	8	Payment proposal automation; Automatic posting of invoices from 3rd party application (e.g. IMOS); Accruals automation; Automatic reclassification of entries for group COA; Cost

OBJECT	ESTIMATED #	COMPLEXITY			SAMPLE PLACEHOLDER OBJECTS
		Low	Medium	High	
					allocation from voyages into PC and internal orders; Synch maintenance between SAP and ship management solution; Extensions of COA for L&S; …
Forms (F)	20	6	10	4	AR invoice form; PO form; Management pack layout; Statutory statement layout; …
Workflows (W)	15	5	5	5	Invoice approval; Payment; Urgent payment; JV entry; Intercompany flow; PR/PO approval; Payroll flow; …
Total	**135**	38	64	33	

The bidder is expected to propose two quantification matrix that will:

- define the criteria and the drivers to allocate a RICEFW in one of the above complexity classes
- define the number of implementation days for each pair of RICEFW/Complexity and the pyramid of allocated professionals by role (program manager, delivery lead, Application/technical Architect, functional SME, Technical SME)
- define the location where those days will be delivered (onsite at client location, remote on bidder premises)

As reference below are indicated the expected table to be received

Complexity	Total Md	PM Allocation %	DL Allocation %	Application/technical Architect allocation %	Functional SME allocation %	Technical SME Allocation %	Change SME Allocation %	Total allocation %
Report - Simple								100%
Report - Medium								100%
Report - Complex								100%
Interface- Simple								100%
Interface- Medium								100%
Interface- Complex								100%
Conversion …								100%
…								100%
Workflow - Complex								100%

Figure 1: Pyramid role allocation by RICEFW/Complexity

Complexity	Driver 1	Driver 2	Driver 3	Driver 4	Driver 5	Driver 6
Driver Description						
Report - Simple						
Driver Lower limit indication						
Driver Upper limit indication						
Report - Medium						
Driver Lower limit indication						
Driver Upper limit indication						
.....						
Driver Lower limit indication						
Driver Upper limit indication						
Workflow - Complex						
Driver Lower limit indication						
Driver Upper limit indication						

Figure 2: Complexity Matrix driver definition

The two above matrixes will be used by the bidder to quantify the effort and pyramid required to deliver the RICEFWs estimated in this proposal.

Deviations in number and complexity on the above RICEFWs table will be managed through a formal change control process. The RICEFWs effort will be managed with a dedicated pool of man-days that would be reallocated (up to the maximum capacity) to the number and complexity of RICFEW agreed at the end of the design phase.

RICEFWs effort consumptions will be split in 60% committed as part of design & implementation and 40% committed as part of additional enhancements & integrations (section 2.16) and it will have to be confirmed by Adnoc before to proceed.

2.5 SAP implementation – Infrastructure & Accesses

All infrastructure, applications, software, and associated licenses required to support the scope of work will be provided by ADNOC. The same applies to access management, where ADNOC will be responsible for the setup and management of the Identity and Access Management (IAM) architecture across L&S and its subsidiaries.

The bidder shall support the following activities

- End-to-end SAP BASIS services, including system management, monitoring, and operational support throughout the duration of the project
- Application security management, including SAP roles and authorizations design and maintenance
- Design and implementation of UI data masking and UI logging for SAP, with detailed requirements to be defined during the Explore phase
- Design and implementation of SAP GRC solutions, including Access Control, Process Control, and Risk Management

2.6 SAP Implementation – Data Cleansing

The bidder shall support ADNOC L&S and the subsidiaries in the enrichment, cleansing and preparation of legacy data prior to the migration into the target OneERP environment.

The objective of this activity is to improve data quality and usability across the group before onboarding into SAP. The scope includes data enrichment and harmonization activities but excludes deduplication initiatives unless explicitly agreed otherwise.

The bidder shall:

- Define the overall data cleansing approach, governance, and execution methodology
- Establish a centralized staging repository / database to consolidate and manage the data to be cleansed prior to migration
- Propose and leverage digital solutions tools to accelerate the activities
- Define cleansing rules, mapping logic, enrichment criteria, and data ownership responsibilities across business stakeholders
- Propose an approach for data scrambling / masking where required to support testing and non-production environment usage while maintaining compliance with ADNOC security requirements
- Support the business in validating the key enriched master data objects including vendors, customers, materials, assets, employees
- Execute at least two (2) iterative cleansing and validation cycles with the business prior to final migration sign-off
- Provide data quality dashboards, exception reports, and tracking mechanisms to monitor cleansing progress and outstanding issues

To provide an indication of the data volumes to be cleansed, the table below outlines the estimated volumes for the key data objects within scope

OBJECT	L&S	Navig8	ZMI
Vendors Master	5,000	1,600	2,875
Customer Master	1,500	2,500	118
Materials Master	500,000 *(60,000 active)*	N/A	547
Employee records	2,000	380	586
Asset Master	10,000	N/A	215
Profit / Cost center	1,500	108	9
WBS element	37,000	N/A	N/A
Bank master data	100	285	37
Purchase info record	5,000	N/A	N/A
Contracts	5,000	N/A	N/A

Cleansing of data for solutions outside the SAP landscape (e.g., IMOS, AMOS, DigitALL Ocean, and all other operational system) is out of scope for the bidder and will be managed directly by ADNOC L&S in coordination with the respective solution providers.

2.7 SAP Implementation – Data Migration

The bidder shall be responsible for the planning, preparation, execution, validation, and cutover of all data migration activities required to support the onboarding of the subsidiaries into the OneERP platform.

The scope of data migration focuses on the extraction, transformation, transport, reconciliation, and upload of data from legacy systems into the target SAP landscape, including the execution of mock migrations, reconciliation cycles, and final cutover activities.

The scope of data migration shall cover the following categories:

- Master Data Objects: *Chart of Accounts, Company Codes, Profit Centers, Cost Centers, Internal Orders keep and WBS elements, Bank master data, Tax codes and configuration elements, Vendor master data, Material master data, Purchasing info records and source lists, Contracts and Long-Term Purchase Agreements, Inventory master data, Customer master data, Employee master data, Payroll-related master data, Asset master data*
- Transactional Data (Open / Active Data): *Open Accounts Payable (AP) and Accounts Receivable (AR) balances, Open General Ledger balances (trial balance migration), Open accruals and provisions, Fixed asset balances and ongoing depreciation values, Open Purchase Requisitions (PRs), Open Purchase*

Orders (POs), Contracts and call-off orders, Goods in transit and pending goods receipts, Current stock balances by location (vessel / warehouse), Open work orders or project-related commitments, all P&L transaction for the ongoing year. CAPEX and OPEX Budget data. Bank balances

- Historical data will remain in the legacy systems in read-only mode and will not be migrated to the target OneERP environment. Historic operational data managed by third-party applications (e.g., maintenance records in AMOS, voyage data in IMOS) will be migrated within their respective applications by the relevant solution providers. This is outside the scope of the SI and will be coordinated by ADNOC L&S directly with each vendor.

To support migration readiness, the bidder shall execute migration rehearsal cycles and provide reconciliation reports validating completeness and consistency of the migrated data before final cutover.

To provide an indication of the data volumes to be migrated, the table below outlines the annual number of financial entries processed by each company

OBJECT	L&S	Navig8	ZMI
Vendors Master	5,000	1,600	2,875
Customer Master	1,500	2,500	118
Materials Master	500,000 *(60,000 active)*	*n/a*	547
Employee records	2,000	380	586
Asset Master	10,000	*n/a*	215
Profit / Cost center	1,500	108	9
WBS element	37,000	*n/a*	N/A
Bank master data	100	285	37
Purchase info record	5,000	*n/a*	N/A
Contracts	5,000	*n/a*	N/A
Purchase orders	20,000	*n/a*	74,842
AR entries	26,000	34,611	3,895
AP Entries	52,000	51,003	70,444
Jornal Entries	30,000	95,484	108,696

Migration of data for solutions outside the SAP landscape (e.g., IMOS, AMOS, DigitALL Ocean, and all other operational system) is out of scope for the bidder and will be managed directly by ADNOC L&S in coordination with the respective solution providers.

2.8 SAP Implementation – Testing

The Project will follow structured testing approach which is comprised of various levels of testing designed to meet the quality assurance objectives of the required work. The following test cycles are considered in this scope of work:

- Unit testing: Each component unit is configured or developed and tested.
- System integration testing: End-to-end business processes are configured and tested.
- User acceptance testing: User acceptance testing conducted for business processes.
- Regression testing: Critical business processes are tested with the automated test scripts available in OneERP
- Defect management
- Performance testing before each Company go-live

The bidder shall use Tricentis Tosca, provided by ADNOC, as the mandatory testing platform across all test cycles. This covers:

- Recording and tracking of test execution progress and results
- Test automation, including the development and maintenance of automated test scripts for regression testing
- Defect logging and traceability

Given the hybrid architecture—where SAP acts as the corporate backbone (Finance, Procurement, Reporting) while operational systems remain the core business execution platforms—testing will focus on end-to-end business processes across the ecosystem. Key areas of focus for end-to-end testing are:

- Finance flow across EyeShare, IMOS and SAP
- Finance and SD flows across BOS and SAP
- Finance and SD flows across DigitALL Ocean and SAP
- Procurement flow across AMOS and SAP
- Payroll flow from external payroll party to SAP

2.9 SAP Implementation - Application Security (Roles and Authorizations Management)

As part of application security, the bidder should cover the following activities:

- Development of Segregation of Duties (SoD) Matrix, starting from the SAP-delivered SoD and tailor it based on Unified ERP requirements.
- Development of SAP Security Baseline template, consisting of the following:
  - Development of SAP Security Roles: A set of SAP Authorization Roles of the various types (Master, Single, Derived and Composite) to include only authorization objects and organization values that are in scope of ERP.
  - Authorization Roles Assignment to Users
  - Security Roles Testing: Roles will be tested to ensure that the users are able to perform their respective task pertaining to the business process.
- Implementation of SAP Governance Risk and Compliance (GRC), consisting of the following:
  - Access Risk Analysis (ARA)
  - Emergency Access Management (EAM)
  - Access Risk Management (ARM)
  - Business Roles Management (BRM)
- Implementation of Single-Sign-On for web scenarios and SAP GUI scenarios

2.10 SAP Implementation – Change management

The bidder shall be responsible for defining and executing a comprehensive Change Management and Training approach to support the successful adoption of the OneERP solution across ADNOC L&S and its subsidiaries. The objective of this workstream is to ensure that impacted stakeholders are adequately prepared, trained, and supported throughout the transformation, enabling a smooth transition to the new processes, operating model, and systems.

The scope of Change Management shall include, but not be limited to, the following:

- Change Impact Assessment: Identification and assessment of impacts across functions, entities, roles, and processes resulting from the SAP implementation and GBS operating model, together with the definition of mitigation actions
- Communication Management: Definition and execution of a structured communication plan, including key messages, communication channels, stakeholder engagement activities, and communication cadence to ensure alignment across impacted stakeholders
- Training Strategy and Planning: Definition of the training approach, including identification of training audiences, training needs, training environments, and delivery methods aligned with the program rollout strategy
- Training Material Development: Preparation of structured training materials and user adoption content across different media and formats proposed by the bidder (e.g., guides, simulations, e-learning, videos, quick reference cards)

- Training Delivery: Delivery of comprehensive training sessions covering system functionality, business processes, and operational procedures for the identified L&S and subsidiaries users
- Vendor Onboarding & Enablement Support: Preparation of onboarding materials and support to ADNOC L&S teams during onboarding of suppliers, vendors, and third parties impacted by the new procurement and collaboration processes
- Continuous Adoption & Digital Guidance Tools: Development of materials and implementation of continuous improvement tools (e.g., SAP WalkMe or equivalent solutions) to support in-system guidance, and continuous learning post go-live

Below are the estimated counts of Super Users and End Users to be considered as part of the TTT and EUT scope

ENTITY	# OF USERS
L&S	500
Navig8	100
ZMI	100

2.11 SAP Implementation – HyperCare

Hypercare support shall be provided following the go-live of SAP across each entity (L&S, Navig8, and ZMI).

Given the hybrid architecture—where SAP acts as the corporate backbone (Finance, Procurement, Reporting) while operational systems remain the core business execution platforms—hypercare will focus on stabilizing end-to-end business processes across the ecosystem.

Hypercare activities shall include, but not be limited to, the following:

- Provision of hypercare support for a period of three (3) months from the go-live date of each entity
- Knowledge transfer and formal handover of project deliverables and solution documentation to the operations team
- Resolution and closure of all defects identified during the hypercare period
- Shadowing and knowledge transfer to ADNOC L&S support teams during the final two (2) weeks
- Monitoring of end-user satisfaction and adoption levels, including the definition and execution of corrective actions where required to improve adoption of the target solution. The bidder shall target a minimum adoption level of 80% across impacted user groups before transition to business-as-usual operations

The hypercare model is expected to operate across three support layers. The bidder shall provide support for Level 2 and Level 3 issues in accordance with the following guidelines:

- Level 1 – Key Business Users & Local IT (L&S and Subsidiaries): Handles user issues, data corrections, and basic process clarifications. No bidder involvement is expected at this level.
- Level 2 – GPOs and IT SMEs: Handles more complex process clarifications and cross-functional issues. The bidder shall provide functional and technical support to assist SMEs in clarifying process flows, system behavior, and solution-related topics.
- Level 3 – Bidder Hypercare Team: The bidder shall be accountable for resolving SAP defects, integration issues, technical incidents, and critical business disruptions

Hypercare shall cover end-to-end processes with key focus across the following domains:

- Finance: SAP and integration with IMOS, BOS, DigitALL Ocean
- Procurement: SAP and integration AMOS
- HR: SAP and integration with subsidiary payroll systems
- Maintenance: SAP and integration with AMOS
- Inventory: SAP, WMS and integration with AMOS
- Integration: CPI, APIs, IDocs

Any defects related to a 3rd party solution will be handled by L&S local IT in alignment with the relevant vendors.

The bidder shall resolve all defects and issues identified within the first ten (10) weeks of the eight (12) weeks hypercare period, ahead of the transition to business-as-usual operations.

2.12 GBS TOM Design

The bidder shall study and design a Global Business Services (GBS) model for Finance and Procurement across L&S and its subsidiaries. The objective of the GBS workstream is to conceptualize a scalable, efficient, and controlled service delivery model leveraging the existing capabilities of the subsidiaries (e.g. the offshore Finance capabilities of Navig8) while enabling consistent service delivery across the L&S group.

As part of the engagement, the bidder will be provided with the target operating model of the future L&S organization, which shall be used as a key input for the conceptualization and design of the GBS model.

The GBS design exercise is expected to be pragmatic and value-driven. There is no predefined mandate to fully centralize or harmonize all processes and activities across the group. The bidder is expected to assess the current operating models, evaluate centralization and standardization opportunities, and propose the target model based on operational value, scalability, governance, and business fit.

To provide context on the current operating model, Finance and Procurement activities across ADNOC L&S and its subsidiaries are organized in a decentralized manner.

- At ADNOC L&S, key Finance processes (AP, AR, Payroll) and Procurement activities (Category Management and Supplier Management) are currently managed by ADNOC HQ Shared Services.
- Navig8 operates a centralized Finance organization based in Mumbai, which manages AP and AR across all its legal entities. This team is structured by areas of expertise (e.g., Commercial Shipping, Bunker Trading), ensuring alignment with the specific business segments it supports.
- ZMI operates through IoT Model (Integrated Operating Teams) that consist of (Finance, Procurement, Marine, Technical, Crewing & HSE) with Finance and Procurement these teams embedded within the business, supported by relatively smaller, locally managed teams. Each IOT team manages a group of vessels creating a focused group of activities and faster turnaround times.

L&S and subsidiary stakeholders will play a critical role throughout the study. Business and functional representatives from the different entities will provide input on the target vision, operational ambitions, constraints, and business requirements, and will actively participate in the review and validation of the proposed operating model. The target GBS design is therefore expected to be developed through a collaborative co-design approach between the bidder and the L&S group stakeholders.

This workstream shall include the following:

1. Target model design
    a. Definition of the overall GBS vision, scope, and service delivery model aligned with L&S transformation objectives
    b. Development of the service catalog of the GBS
    c. Identification of the processes to be in scope for GBS (e.g., AP, AR, GL transactional activities, procurement operations, etc.)
    d. Development the operating model and service delivery structure (centralized, hybrid, or federated model) across L&S and subsidiaries
    e. Assessment of the of optimal GBS location strategy (onshore, offshore, or hybrid)
    f. Definition of the sourcing approach (in-house vs outsourced vs hybrid model)
    g. Identification of Automation / AI opportunities across these functions
2. Organization design
    a. Definition of the GBS organizational structure, including roles, responsibilities, and reporting lines

   b. Definition of interlocks between GBS and the retained organization with clear segregation of duties
   c. Sizing of the target organization
3. Service Management Framework
   a. Definition of SLA and OLAs and service performance targets
   b. Definition of governance forums and performance review cadence (e.g., operational reviews, service reviews) with the related reporting frameworks
   c. Definition of the service evolution and governance framework, including mechanisms to govern service scope changes, continuous improvement initiatives, and changes to the intercompany back charging
4. Transition and Implementation Roadmap
   a. Development of the establishment of the GBS including hiring and transition strategy from current entities to the GBS organization
   b. Development of a phased transition roadmap aligned with the ERP rollout
   c. Identification of transition risks and define mitigation strategies
   d. Design of the high-level change plan in alignment with the ERP rollout

2.13 Infrastructure design – Infra & Cybersecurity current state assessment

As part of the program, the Bidder shall conduct a detailed infrastructure, application, and cybersecurity landscape assessment of Navig8 and ZMI. The objective of this assessment is to establish a clear, evidence based understanding of the current state across technology, security, operations, and governance domains that may impact ERP enablement, integrations, and long-term sustainability.

On top of that, as a result of the assessment the bidder shall support the design of the target state architecture, migration planning, risk mitigation, and go live decision making.

The current state assessment shall include, but not be limited to, the following domains.

1. Infrastructure, Hosting, and Cloud Landscape
   a. On premise, cloud, and hybrid infrastructure landscape
   b. Hosting models for ERP, non-ERP, Vessel, OT and supporting workloads
   c. Use of public cloud (IaaS, PaaS) and SaaS platforms
   d. Infrastructure ownership, support boundaries, and lifecycle status
2. Business Applications & Application Lifecycle
   a. Business application landscape, including ERP, non-ERP, dependent and adjacent systems
   b. Application criticality, lifecycle stage, and technical debt considerations
   c. Ownership and vendor support models
3. Enterprise & Solution Architecture
   a. Existing enterprise architecture principles and patterns
   b. Alignment (or misalignment) between applications, data, and infrastructure
   c. Architecture documentation maturity and governance processes
4. System Integrations & APIs
   a. Integration technologies, middleware platforms, and data exchange mechanisms
   b. API exposure, authentication models, and integration security
   c. Integration design standards and governance practices
5. Network Architecture & Segmentation
   a. Core, access, and edge network design
   b. Segmentation between IT, OT, and external environments
   c. Perimeter controls, firewall rules, and remote access paths
6. Vessel Infrastructure & Connectivity
   a. Shipboard IT and OT environments

   b. Connectivity models between vessels and shore (satellite, terrestrial, hybrid)
   c. Resilience, latency, and operational dependencies
7. Capacity, Performance, and Scalability
   a. Resource utilization across compute, storage, and network
   b. Performance constraints affecting ERP integrations
   c. Scalability limitations relative to future growth
8. Operating Locations & User Base
   a. Geographic footprint
   b. Operating offices, ports, vessels, and remote sites
   c. User population size and access patterns
9. Devices & IT Asset Inventory
   a. End user devices, servers, and network assets
   b. Asset ownership and lifecycle management
   c. Configuration standards and patching posture
10. Identity and Access Management (IAM)
   a. IAM architecture and directory services
   b. User provisioning and lifecycle processes
   c. Role models and access governance practices
11. Authentication & MFA Controls
   a. Authentication mechanisms used today
   b. MFA coverage, enforcement gaps, and exceptions
   c. Alignment with modern identity security practices
12. Privileged Access & Administrative Governance
   a. Privileged accounts and service accounts
   b. Credential management and rotation practices
   c. Use (or absence) of Privileged Access Management solutions
13. Vendor & Third Party Access
   a. External access models
   b. Shared credentials, VPN access, and unmanaged accounts
   c. Governance and approval processes
14. Cybersecurity Posture & Threat Landscape
   a. Security tools and controls in place
   b. Vulnerability, threat, and exposure posture
   c. Recent incidents or known risk themes
15. SOC & GNOC Operations
   a. Security monitoring and response capabilities
   b. Network operations visibility
   c. Escalation paths and integration with third party providers
16. Monitoring, Logging, and Reporting
   a. Log sources and retention
   b. Integration with SIEM or monitoring platforms
   c. Gaps in visibility or auditability
17. Data Security, Ownership & Residency
   a. Data classification and ownership models
   b. Data residency and sovereignty considerations
   c. Backup, retention, and recovery practices
18. IT Operating Model
   a. Centralized vs decentralized IT structures including outsourced and managed services
   b. Roles, responsibilities, and decision authority

19. End User Support & SLAs
    a. Service desk model and coverage
    b. Incident handling timelines
    c. Vendor support agreements
20. Incident, Change & Development Governance
    a. Change management frameworks
    b. Release and deployment practices
    c. Controls over production environments
21. Audit, Compliance & Regulatory Alignment
    a. Internal and external audit posture
    b. Compliance with industry and regulatory requirements
    c. Existing gaps or remediation activities
22. Disaster Recovery & Business Continuity
    a. DR architecture and recovery objectives
    b. BCP maturity and testing frequency
23. OT & Navigation Systems (Where Applicable)
    a. Navigation systems including ECDIS, GPS, AIS, and Radar
    b. OT network segmentation and isolation from IT environments
    c. Integration points between OT and enterprise systems
24. Policies, Standards, and Documentation
    a. Information security policies and standards in place
    b. Architecture and operational standards maturity
    c. Gaps between documented policy and implementation

Upon completion of the current-state assessment, the bidder shall produce the following formal deliverables:

- Gap Analysis including
  - Report on a gaps against ADNOC Baseline Cybersecurity, Infrastructure, and Regulatory Standards
  - Identification of non-compliances, risks, and dependencies impacting the new ERP, non-ERP and supporting infrastructure
- Mitigation Roadmap & Interim Controls including
  - Definition of mitigation actions for identified gaps
  - Proposal of interim solutions where full remediation is not immediately feasible
  - Articulation of risk ownership and timelines
- Target State Architecture aligned with ADNOC Cybersecurity, Infrastructure, and Cloud standards covering
  - ERP and non-ERP applications
  - Infrastructure, cloud, and network layers
  - Identity, access, and security controls
- Migration Strategy for all in scope infrastructure, platforms, and applications including sequencing, dependencies, and risk considerations while ensuring business continuity and alignment to the ERP deployment timeline
- Operating & Support Model for SAP (ERP) services, ERP-connected non-ERP systems, Vessels and OT systems and covering roles, SLAs, escalation models, and integration with ADNOC support structures

2.14 Infrastructure design – Non-ERP Application Hosting Strategy

The bidder shall produce, as part of the SAP OneERP target-state design, a hosting strategy per ERP-connected application, covering hosting model, SAP integration approach, identity integration, security controls, migration approach (if applicable), and cutover dependencies.

For each application, the target hosting model may include migration to an ADNOC-managed cloud environment, retained hosting governed by ADNOC security controls, or a hybrid model approved by ADNOC.

This section covers explicitly ERP-connected non-SAP applications that must be enabled as part of the transformation, including:

- From Navig8: IMOS, EyeShare, HiBob, Bunker Operating System
- From ZMI: AMOS, DigitalOcean

For these applications, a hosting pattern is mandated. The bidder shall define and propose an end-state application and cloud hosting strategy as part of the SAP OneERP target-state architecture.

The proposed hosting strategy shall:

- adhere to ADNOC Cloud Strategy and ADNOC Group Digital Cybersecurity Standards;
- enforce mandatory security controls such as Multi-Factor Authentication (MFA), encryption, secure logging, and approved access mechanisms irrespective of hosting model; and
- form an explicit part of the SAP OneERP end-state architecture and not a temporary or tactical arrangement.

The broader consolidation of network infrastructure and non-ERP applications (including productivity tools, collaboration platforms, and general IT workloads) remains explicitly out of scope for this engagement and will be addressed through separate initiatives.

All proposed hosting models shall be subject to review and formal approval by ADNOC, with ADNOC retaining final authority over hosting, security, and risk acceptance decisions.

Mandatory controls, regardless of hosting model, shall include ADNOC-approved identity and access management, MFA enforcement, encryption in transit (TLS 1.2+) and at rest (AES-256 or equivalent), centralized RBAC/ABAC, and security logging aligned to ADNOC SOC requirements.

Below a few considerations to be considered by the bidder

- Secure remote access for Navig8 and ZMI users to SAP OneERP and ERP-connected applications shall be provided using one of the following ADNOC-approved models or a newer model that can be derived from the bidder cybersecurity assessment and end state architecture:
    - Virtual Desktop Infrastructure (VDI), such as Azure Virtual Desktop, using ADNOC-managed desktop images with enforced session controls including clipboard restriction, auto-timeout, and no USB redirection.
    - Site-to-site IPSec VPN using dedicated VLANs for Navig8 and ZMI traffic, with no unrestricted access to the broader ADNOC internal network
- Legacy ERPs (e.g. Microsoft Dynamics) shall remain hosted within existing Navig8 and ZMI infrastructure and shall be locked to read-only mode on the agreed SAP OneERP cutover date to prevent parallel transactional processing.

2.15 Infrastructure design – ERP Cybersecurity Assessment

The bidder shall conduct a comprehensive ERP assessment along with the complete infrastructure assessment described in the previous sections of the document, end-to-end cybersecurity assessment of the Navig8 and ZMI environments, strictly scoped to SAP OneERP access, integrations, data flows, and ERP-dependent business operations.

The assessment shall evaluate the current state, control maturity, and cybersecurity risk posture of all components that could directly or indirectly impact the confidentiality, integrity, or availability of SAP OneERP.

The assessment shall cover identity and access management, endpoint security, network connectivity, existing identity platforms within Navig8 and ZMI, SAP security controls, and cloud services that support SAP or ERP-related integrations.

All findings shall be benchmarked against ADNOC Group Digital Cybersecurity Standards, clearly classified by severity, and mapped to their potential impact on SAP OneERP.

The bidder shall produce a formal SAP-scoped cybersecurity assessment report, detailing current-state observations, identified risks, gaps against ADNOC standards, and required remediation actions. Completion and acceptance of this assessment is a prerequisite to SAP access enablement and ERP cutover.

SAP OneERP go-live shall be dependent on the completion of the cybersecurity assessment, the implementation of the target state, the remediation of all ERP-blocking risks are remediated, the validation of access controls, the operationalization of logging, and the obtainment of formal approval from ADNOC Digital Cybersecurity.

Guidelines for identity Authority and Governance

All SAP OneERP users across ADNOC L&S, Navig8, and ZMI shall be provisioned under a unified and ADNOC-governed identity model. Users shall either be provisioned directly within ADNOC Microsoft Entra ID or governed through an ADNOC-approved federated or synchronized identity model.

ADNOC shall remain the authoritative identity governance entity for SAP access, including control over authentication policies, authorization models, identity lifecycle management, and privileged access governance.

Local, unmanaged, or independently governed SAP user accounts are strictly prohibited.

Guidelines for Tenant Strategy

SAP OneERP shall operate exclusively within an ADNOC-controlled tenant environment. Any Navig8 or ZMI users accessing SAP shall be subject to ADNOC tenant-level policies, Conditional Access controls, logging, and audit mechanisms.

Standalone Navig8 or ZMI tenants shall not independently govern, authorize, or manage SAP access. Any transitional or federated access models must be explicitly documented and approved by ADNOC, with governance authority retained by ADNOC at all times.

Guidelines for Cloud Strategy and Governance (SAP Scope)

All cloud resources supporting SAP OneERP, including ERP platforms, integration middleware, interfaces, and ERP-dependent workloads, shall reside within ADNOC-owned or ADNOC-governed cloud subscriptions.

ADNOC shall retain privileged administrative access, role-based access control (RBAC) authority, and policy enforcement rights, including policy-as-code.

Where Navig8 or ZMI cloud services are required to support SAP integrations, such services shall operate within an ADNOC-governed cloud operating model. Independent or unmanaged cloud environments supporting SAP access are not permitted.

ERP integration platforms and middleware used to connect SAP with in scope applications shall be treated as ERP dependent workloads and governed under the same ADNOC cloud, identity, and cybersecurity standards

Guidelines for Mitigation and Remediation

The bidder shall develop a comprehensive mitigation and remediation plan addressing all SAP-impacting cybersecurity risks identified through the assessment.

All High and Critical findings impacting SAP OneERP shall be fully remediated prior to ERP cutover.

Risk acceptance or deferral shall only be permitted with formal written approval from ADNOC Digital Cybersecurity. Failure to complete remediation constitutes a blocking dependency to SAP go-live.

Guidelines for Identity Integration and Secure SAP Access

All SAP OneERP access shall be implemented exclusively through ADNOC-approved identity mechanisms.

Mandatory controls include Multi-Factor Authentication (MFA), Conditional Access, least-privilege authorization, and centralized governance under ADNOC identity platforms.

Alternative authentication methods, local credentials, or unmanaged access paths shall not be permitted.

Guidelines for Joiner–Mover–Leaver (JML)

The bidder shall implement automated Joiner–Mover–Leaver (JML) controls integrated with the ADNOC Identity Provider to govern the SAP access lifecycle.

Automated provisioning, role modification, and immediate de-provisioning shall be enforced for all SAP users. Manual or ad-hoc SAP access administration is prohibited.

Guidelines for Logging, Monitoring, and Visibility

The bidder shall ensure comprehensive security telemetry for SAP OneERP, including SAP authentication, authorization, and integration logs.

All relevant logs shall be forwarded to the ADNOC Security Operations Center (SOC) SIEM for centralized monitoring, correlation, and incident response.

Guidelines for Data Protection and Residency

All SAP OneERP data shall be protected using TLS 1.2 or higher for data in transit and AES-256 encryption for data at rest.

SAP data, backups, and operational logs shall reside within UAE-based data centers unless explicitly approved otherwise by ADNOC.

All data created, processed, or exchanged as part of SAP OneERP business processes shall be classified as ADNOC data and governed in accordance with ADNOC data classification and protection policies, irrespective of the hosting location

2.16 Additional Enhancements & Integrations

ADNOC expects the bidder to allocate 60% of the RICEFWs as part of design & implementation scope and the remaining 40% into this additional enhancements & integrations scope line item and is going to be managed through complexity matrix and effort per complexity item (matrixes provided in section 2.4 SAP Implementation - RICEFWS).

Bidder to clearly propose the mandays & number of RICEFWs being considered for the remaining 40% of the RICEFWs implementation.

Considering the continuous demands for requirements and over the duration of the agreement, ADNOC expects bidder to provide the rate card for T&M model and will follow purely milestone payments.

NOTE:

- It is assumed that the Mandays defined per Rate Card Role in the Schedule of Fees for Optional Scope / Time & Material line items are indicative and for budgetary purpose only. When staffing each activity, ADNOC reserves the right to request revised mandays based on ADNOC's needs and subject to the remaining amount left for the Optional Scope / Time & Material line items.
- ADNOC reserves the right to consume the Optional Scope / Time & Material amount defined in the Schedule of Fees at any time during the AGREEMENT duration, even if the specific Optional Scope / Time & Material line items in the Schedule of Fees specifies a certain contract year. This means ADNOC can pull forward or pushback when the Optional Scope / Time & Material budget is planned to be consumed.
- From time to time the PARTIES may agree on converting a portion of the T&M budget specified in the Schedule of Fees as Optional Scope / Time & Material, to allow CONTRACTOR to provide packaged Milestones-based Services or Capacity based Services. In such cases, the PARTIES shall agree on the Scope Element with the description of the scope to be provided and the milestones schedule or capacity invoicing schedule. The payment(s) will be provided by ADNOC based on the acceptance of the milestone certificate(s).

3 AI-Enabled Transformation

The System Integrator (SI) is required to deliver the SAP program as an **AI-enabled transformation**, embedding **AI agents** both:

- within **business operations (run layer)**
- across **delivery lifecycle activities (build layer)**

As part of the AI enabled transformation Adnoc expect the following benefits:

- to transition from traditional ERP implementation to an **autonomous ERP model**, where AI agents augment or replace manual tasks, improve decision-making, and enable continuous optimization
- to simplify and accelerate the delivery of the project

3.1 Scope and expectations

The SI, for processes indicated as re-design, shall propose, design, build, and deploy **AI agents embedded into SAP processes** to enable autonomous and intelligent operations, where enabled as part of the SAP standard solution.

These agents must:

- Execute end-to-end process steps with minimal human intervention
- Orchestrate workflows across SAP (S/4HANA, Ariba, SuccessFactors) including integrations
- Continuously learn from historical data and user interactions

- Operate within defined governance and control frameworks

3.2 Core capabilities requirements

AI-Assisted Process Discovery and Design

- AI-driven process mining and analysis
- Automated extraction of requirements from:
  - Documents
  - workshops
  - legacy systems
- AI-generated:
  - Business process models
  - Fit-to-standard recommendations
  - Functional specifications

AI-Driven Development (Build Phase)

- GenAI-assisted generation of:
  - Functional and technical specifications
  - ABAP / BTP code artifacts
  - Integration mappings and APIs
- AI-supported code review and quality validation
- Automated documentation generation

AI-Based Testing and Quality Assurance

- Automated generation of test cases from requirements
- Predictive defect detection and root cause analysis
- Intelligent test coverage optimization

AI-Enabled Data Migration and Preparation

- Intelligent data profiling, cleansing, and mapping
- AI-driven identification of:
  - Data inconsistencies
  - Duplicate records
  - Data quality issues
- Automation of migration reconciliation and validation

AIOps and Hypercare Automation

- AI-driven monitoring of system stability post go-live

- Predictive incident detection and automated resolution
- Self-healing integrations and workflows

3.2 Delivery Model requirements

The SI shall:

- Establish **dedicated AI delivery pods**, including:
  - AI architect/s
  - SAP BTP / AI engineer/s
- Integrate AI capabilities into:
  - Delivery model
  - DevOps / MLOps pipeline for the Hypercare
- Ensure reuse of AI assets across phases and entities

3.4 Tooling Requirements

The SI must clearly define:


- AI / GenAI tools leveraged (SAP BTP AI, external platforms, etc.)
- Integration with ADNOC enterprise platforms (e.g., data platforms, cloud)
- Automation and orchestration tools

3.5 AI Deliverables (build Layer)

- AI-enabled delivery methodology
- AI toolchain and architecture
- AI-generated design and documentation assets
- Test automation framework
- Data migration and quality framework
- AIOps model for post go-live support

3.6 ADNOC AI Reference Architecture

Bidder to consider below most updated version of ADNOC AI Reference Architecture (subject to change) in proposing any AI tools/solutions.

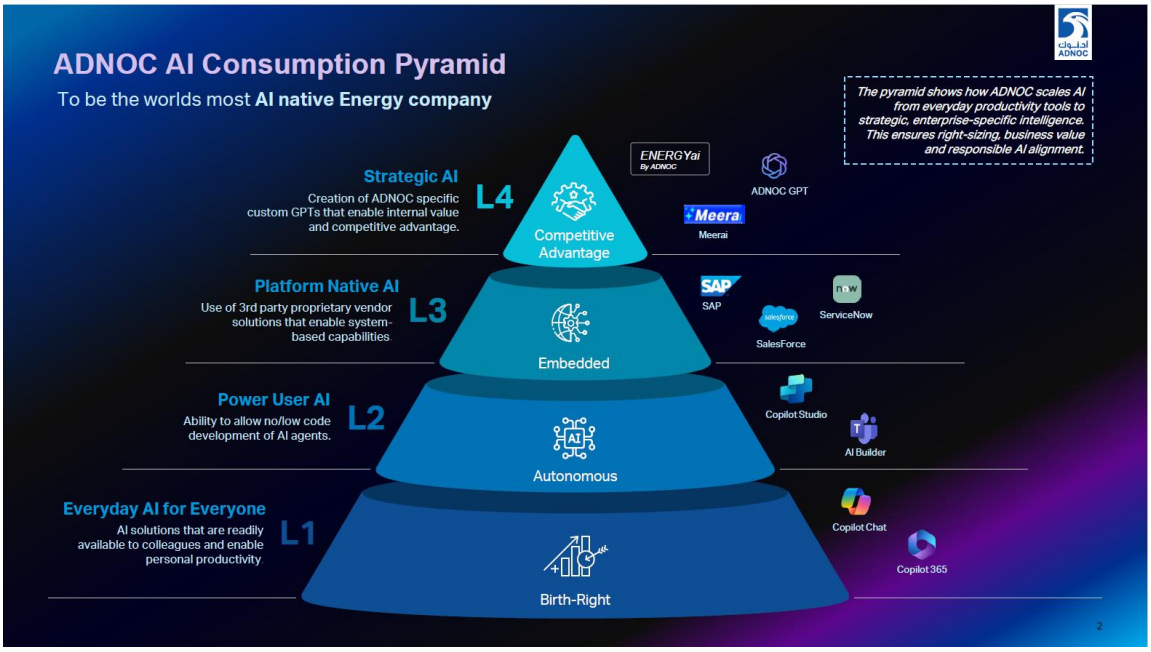




4 Project methodology

4.1 Project plan

The activities described in the previous chapter shall be managed according to the high-level plan displayed below. ADNOC L&S is looking to complete the design phase of the ERP and the GBS organization in 2026 and then to complete the roll out in phase across L&S and subsidiaries by the

The bidder will work with the assigned ADNOC L&S project manager to update, detail, finalize and maintain a project plan, including an ongoing timeline. Bidder and ADNOC L&S project manager will review, on a regular basis, progress against the project plan along with any associated issues and risks.

Material changes to the timeframes of the project in respect of any requirements or constraints other than those specified within this SOW, together with any consequential changes to services and/or scope of the SOW, will be managed by a CONTRACT VARIATION process so that impacts of proposed changes can be agreed upon and an informed decision made in response to the proposed change.

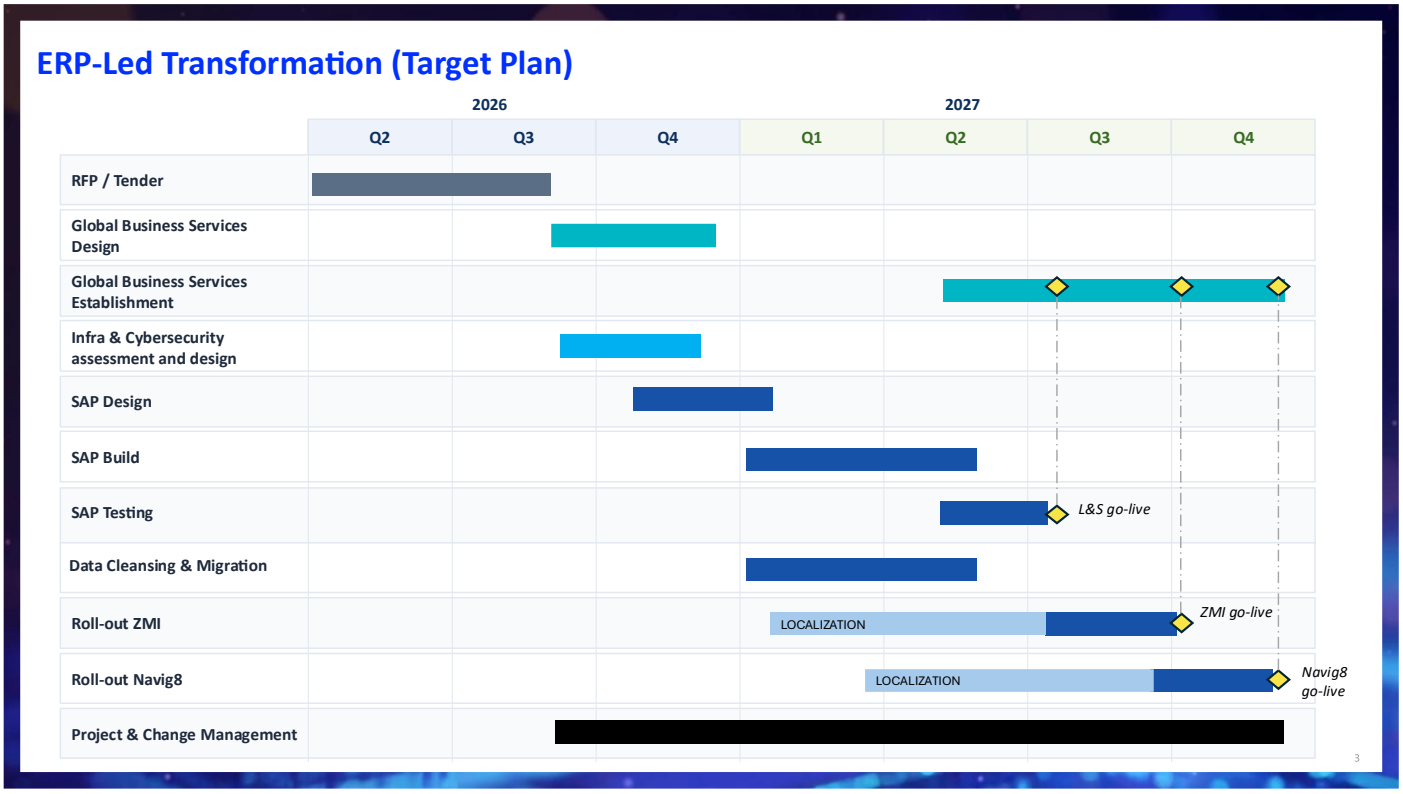

4.2 RACI

ADNOC L&S acknowledges that the bidder ability to meet its obligations under this SOW is dependent on the performance by ADNOC L&S and subsidiaries of their own obligations as set out in the below RACI matrix. Changes to any bidder responsibilities shall be handled in accordance with a new SOW to be agreed between the parties, considering timeline changes, resource availability and cost implications.

GROUP	ACTIVITY	L&S Program Team	L&S Business	BIDDER
Project Management	Define overall program plan	A	I	R
Project Management	Handle project plan, monitor activities and provide status update	I	I	R, A
Project Management	Identify risks and mitigation actions	C	I	R, A
ERP Design	Perform fit-to-gap assessment and develop BPD and KDDs documentation for all processes that require adaptation, enhancement or re-engineering	C, I	I	R, A
ERP Design	Review and sign-off BPDs and KDDs	R, A	I	I
ERP Design	Confirm the RICEFW scope for the Build Phase	C, I	I	R, A
ERP Design	Assess impacts of new ERP processes on the configuration of the business solutions (e.g. IMOS, AMOS, …)	R, A	I	I
ERP Design	Provide enterprise structure to be setup in SAP (e.g. Legal entities, plants, COA, …)	R, A	I	C, I
GBS TOM	Develop target model of the GBS organization across Finance and Procurement	C	I	R, A
GBS TOM	Review and sign-off the GBS TOM	R, A	I	I
GBS TOM	Onboard the required people, setup and implement the GBS TOM	R, A	I	I
Infrastructure	Design of the target infrastructure and IAM including hosting strategy for ERP related applications and migration strategy	C, I	I	R, A
Infrastructure	Setup of the required hosting environment, migration of the applications and handling of IAM	R, A	I	I
Functional specification	Develop functional specifications documentations for the identified RICEFW	C, I	I	R, A
Functional Specifications	Coordinate with 3rd parties solution provider to share design and integration changes	R, A	I	I
Functional Specifications	Sign-off the FSD documents	R, A	I	I
BASIS	Setup, prepare and administer the required environment	R, A	I	I
BASIS	Configure Basis and handle transport and change management	C, I	I	R, A
Build	Build SAP configuration and run Unit Test	I	I	R, A
Build	Develop SAP RICEFW Technical specifications	C, I	I	R, A
Build	Build SAP RICEFW and run Unit Test	I	I	R, A
Build	Build SAP Security Roles Build and run Unit Test	I	I	R, A
Build	Develop specification for 3rd parties solutions impacted by SAP changes	R, A	I	I
Build	Coordinate build of 3rd parties solutions changes as per requirements	R, A	I	I
Data cleansing	Develop data cleansing strategy and approach	I	C	R, A
Data cleansing	Setup environment to host and manipulate data	I	I	R, A
Data cleansing	Extract and provide required data	C	R, A	I
Data cleansing	Run iteration of data enrichment and cleansing and provide regular reporting on the activities	I	C	R, A

GROUP	ACTIVITY	L&S Program Team	L&S Business	BIDDER
Data cleansing	Sign-off data cleansing activities and readiness for migration	C	R, A	I
Data migration	Develop data migration strategy and approach	C, I	I	R, A
Data migration	Setup templates for the collection of the required data to be migrated	I	I	R, A
Data migration	Extract and share data to be migrated from the legacy systems	R, A	I	C
Data migration	Handle the migration of the data of the business solutions (e.g. IMOS, AMOS, …) in the new environment	R, A	I	I
Data migration	Execute upload of data into the target ERP	C	I	R, A
Test	Define overall test strategy and plan	A	I	R
Test	Develop test scripts	I	I	R, A
Test	Execute system integration tests	I	I	R, A
Test	Coordinate third parties vendors during the execution of SIT to test the end to end flows	R, A	I	C, I
Test	Develop SIT execution status report	I	I	R, A
Test	Develop User acceptance test scenarios	C, I	I	R, A
Test	Execute UAT	R, A	I	C, I
Test	Maintain UAT execution status report	I	I	R, A
Test	Sign-off completion of test and readiness to go-live	R, A	I	I
Deploy & Hyper care	Define overall cut-over strategy and plan including sequencing of the company go-live	A	I	R
Deploy & Hyper care	Handle cutover progress status report	C, I	I	R, A
Deploy & Hyper care	Handle HyperCare support	I	I	R, A
Change management	Identify and assess impacts across functions, entities and roles	A	I	R
Change management	Identify change mitigation actions	A	I	R
Change management	Define and execution of a structured communication plan	C, I	I	R, A
Change management	Definition of the training approach and plan	A	I	R
Change management	Develop training materials on SAP	C, I	I	R, A
Change management	Deliver Train the trainer and end user training on SAP	I	I	R, A

4.3 Deliverables

This section outlines the key deliverables expected from the bidder throughout the program lifecycle. The bidder shall be responsible for the preparation, validation, and delivery of at list (but not limited to) of the following deliverables

DELIVERABLE	DESCRIPTION	DOCUMENT FORMAT
Program plan	Detailed project plan outlining phases, milestones, timelines, dependencies, and resource allocation across ERP and GBS workstreams	Project (.mpp) / Excel (.xls)
Program charter	Formal definition of program objectives, governance structure and cadence, key stakeholders, and success criteria	Word (.docx)
Program tracker	Formal definition of program objectives, scope, governance structure, key stakeholders, and success criteria	MS Project (.mpp) / Excel (.xlsx)
GBS TOM	GBS target operating model, including scope, service catalog, organizational structure, roles and responsibilities, governance, and service management framework	Powe point (.pptx)
BPD	Business process design documents detailing of end-to-end business processes in scope including key design decision for the configuration in SAP	Word (.docx)
Technical architecture	Formalization of system architecture, including ERP landscape, integration approach, infrastructure, and security considerations	Word (.docx)
RTM	Mapping of business requirements to functional and technical design elements, ensuring full traceability throughout the lifecycle	Excel (.xlsx)
RICEFW Log	Consolidated inventory of all RICEFW objects, including classification, description, priority, and implementation status	Excel (.xlsx)
FSD	Detailed functional design documents for all configuration and custom developments (RICEFW)	Word (.docx)
Cleansed data for migration	Cleansed data set for the upload into the new system	Excel (.xls)
SIT	Test scenarios, scripts, execution results, and defect logs for system integration testing	Word (.docx)
RT	Test scenarios, scripts, execution results, and business sign-off documentation for Regression testing (RT) at the time of Hypercare	Word (.docx)
UAT	Test scenarios, scripts, execution results, and business sign-off documentation for user acceptance testing	Word (.docx)
Cutover Tracker	Detailed cutover strategy, activities, sequencing, responsibilities, and tracking of execution during go-live	Excel (.xlsx)
Training material	Structured training content for Train-the-Trainer and End User Training, including user guides, manuals, and digital learning materials	Word (.docx)/ Power point (.pptx) and further media suggested by the bidder (e.g. video, ..)
Go-live report	Summary of go-live activities, system readiness, issues encountered, and confirmation of successful deployment	Word (.docx)
Hypercare report	Summary of post-go-live support activities, issue resolution, system stabilization status, and transition to steady-state operations	Word (.docx)/ Power point (.pptx)
Change plan	Definition of change management approach, including stakeholder engagement, communication strategy, and adoption activities	Word (.docx)/ Power point (.pptx)
Communication	Communication strategy, key messages, communication calendar, and supporting materials	Word (.docx)/ Power point (.pptx) and further media suggested by the bidder (e.g. newsletter, …)
Change impact assessment	Assessment of impacts on processes, roles, and organization, including mitigation actions and transition considerations	Word (.docx)/ Power point (.pptx)
Infra and Cybersecurity assessment	Report on Infra, Security and Network gaps of Navig8 and ZMI against ADNOC Baseline Cybersecurity, Infrastructure, and Regulatory Standards including also the identification of non-compliances, risks, and dependencies impacting the new ERP, non-ERP and supporting infrastructure	Word (.docx)/ Power point (.pptx)
Infra and cybersecurity Target state	Report with Target State Architecture and IT operating model covering i) ERP and non-ERP applications ii) Infrastructure, cloud, and network layers iii)Identity, access, and security controls and including the migration strategy	Word (.docx)/ Power point (.pptx)


4.4 Program organization

The program will be delivered through a structured and integrated organization model designed to ensure strong governance, clear accountability, and effective coordination across business and technology

At the core of the model is central Program Management, led by a Program / Transformation director, responsible for overall governance, planning, and execution oversight across all workstreams. The organization is structured around a set of key pillars:

- Program Management Office (PMO): Provides day-to-day program oversight, including planning, tracking, risk and issue management, and coordination across all stakeholders.
- GBS Target Operating Model (TOM): Leads the design of the future operating model for Finance and Procurement, ensuring alignment between organizational design, processes, and ERP capabilities.
- Functional Streams: Drive the end-to-end design and implementation of ERP processes across core domains (Finance including Sales, HR, Procurement & Inventory including maintenance), ensuring business requirements are translated into system solutions. Each functional stream will be led by a Global Process Owner (GPO), who will act on behalf of all entities and ensure alignment and standardization of processes across L&S and its subsidiaries. The GPO will be supported by Subject Matter Experts (SMEs) and representatives from the different business segments (e.g., Commercial Shipping, Ship Management, Offshore), ensuring that segment-specific requirements are captured and appropriately reflected in the solution design
- Horizontal / Cross-Functional Streams: Enable delivery across all functional areas, including Data Migration, Integration & Development, Testing, Infrastructure & Identity Management, Third-Party Solutions, and Rollout & Cutover.
- Architecture: Ensures consistency and integrity of the overall solution design, including application, integration, and technical architecture.
- Change Management Office (CMO): Supports organizational readiness and adoption through structured change management, communication, and training activities.

The program is delivered through a joint business–technology–bidder model, with clear roles across business leads, SMEs, technical teams, and bidder resources to ensure alignment between functional requirements, system design, and implementation

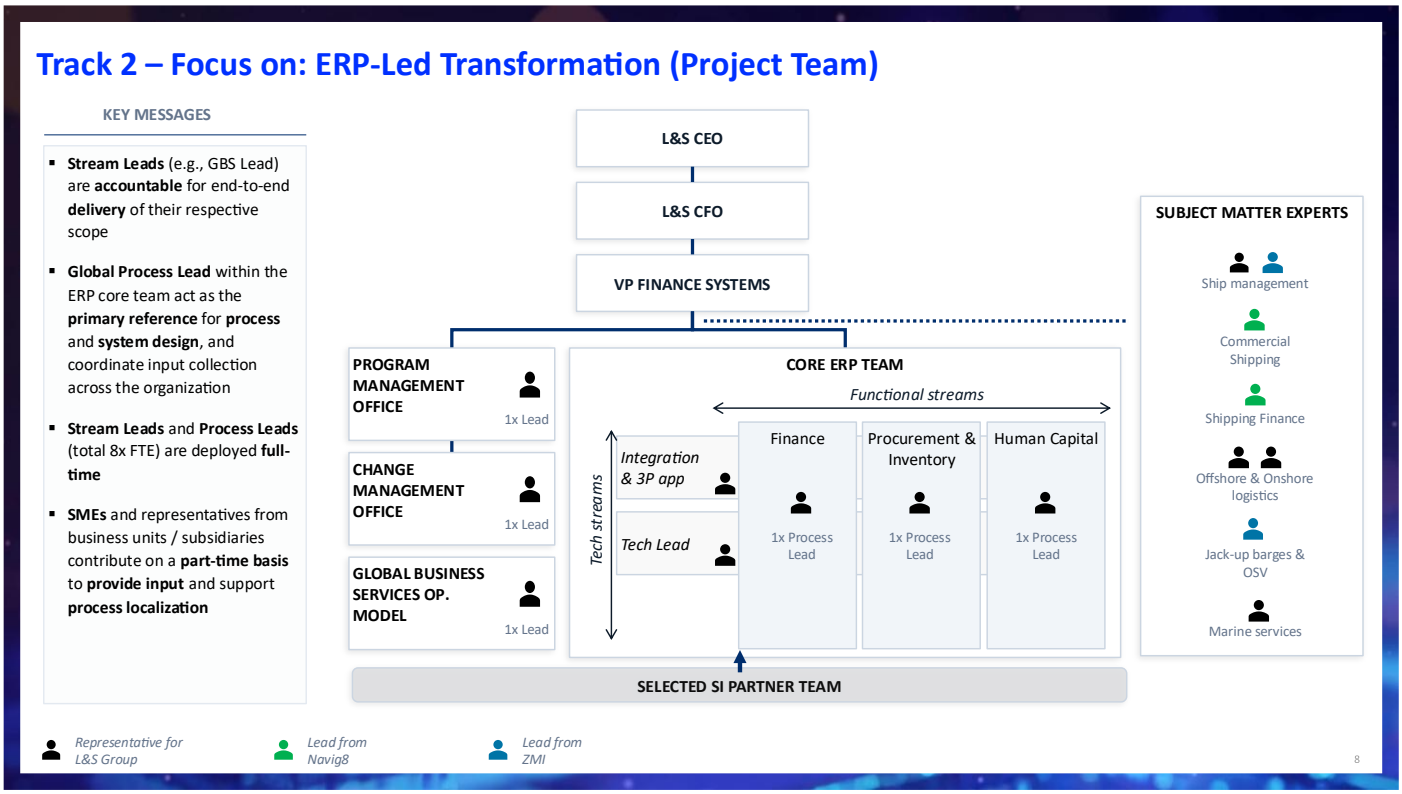


4.5 Program governance

The program will be governed through a structured and tiered governance model designed to ensure clear decision-making, effective oversight, and timely resolution of issues across all phases of the transformation.

This model establishes a balance between strategic direction and day-to-day execution by defining distinct forums for executive alignment, program oversight, solution control, and operational coordination. It enables consistent engagement of business and technology stakeholders across L&S and its subsidiaries making sure that business nuance are properly captured in the solution design.

The program will be coordinated by ADNOC HQ on behalf of ADNOC L&S and will leverage the governance mechanisms, standards, and delivery controls already established as part of the ADNOC OneERP program. This includes alignment with existing governance forums, design authority principles (tailored to L&S objectives), architecture standards, and program management practices to ensure consistency with the broader ERP landscape and accelerate delivery.

An overview of the governance structure, including the main forums and their interactions, is illustrated in the figure below

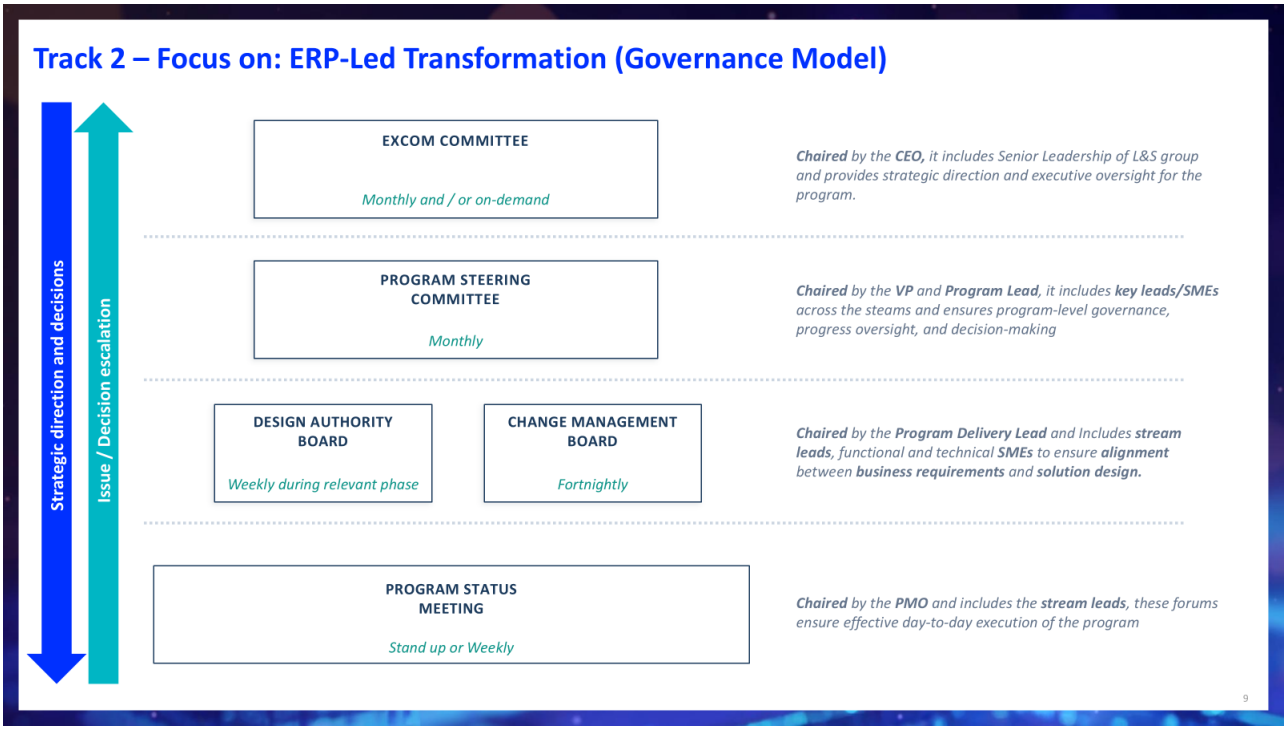

4.6 Collaboration with 3rd Parties

ADNOC L&S will be responsible for coordinating with key third-party solution providers that require integration with SAP. The bidder is expected to collaborate effectively with these parties and define the delivery and collaboration model, ensuring alignment across all stakeholders and facilitating the design and implementation of integration solutions with SAP.

Below is the list of key third-party providers expected to be involved more heavily throughout the engagement.

3rd Party	DESCRIPTION
Veson	Provider of the IMOS platform used for commercial shipping operations, including voyage management, chartering, and voyage accounting. Integration with SAP will focus on financial postings, accruals, invoicing, and master data alignment
EyeShare	Provider of workflow automation to orchestrate invoice processing. Integration with IMOS and SAP will focus on invoice posting
SpecTech / MaryApp	Providers of ship management systems supporting maintenance, inventory, and procurement for vessel operations. Integration with SAP will cover procurement and inventory synchronization, and exchange of master data
DigitALL Ocean	Provider of offshore and logistics operational systems supporting OSV activities. Integration with SAP will focus on integration of contracts and billings
HR and Payroll vendor	Provider of HR solution (e.g. HiBob) and / or payroll services. Integration with SAP will focus on time management and journal entries
SmartPort	Provider of Petroleum Port Operations solution. SmartPort is a digital platform that automates and optimizes end-to-end marine and port operations across key ADNOC petroleum ports. It delivers real-time operational visibility, intelligent resource planning, and automated billing through seamless integration with ONE ERP and PMIS, driving efficiency, safety, and scalable growth while reducing manual effort and operational risk.


4.7 Standards and Guidelines of OneERP

Requirements and demand management


The following activities need to be covered under Requirement and Demand Management processes

- Engage respective business teams and stakeholder(s) to understand their processes and effectively capture their business requirements
- Design, Solution and Implement enhancements and improvement to the OneERP Solution in area in scope
- Perform process improvement and gap analysis on current implementation to bring positive changes to the business processes through system enhancements.
- Design, code, test, debug, install and document the enhancements for the different SAP modules in scope
- Actively support integration projects from gathering business requirements to go-live and post-implementation support
- Develop detail functional and technical specifications
- Review program codes and correct ABAP program errors
- Develop technical specification and estimations for assigned project
- Work in compliance with the programming and documentation standards.
- Ensure that SAP Best Practices are adhered to and followed at ADNOC.
- Flexibility to adjust to multiple demands, shifting priorities, ambiguity and rapid change.
- Provide clarity to business users on the delivery of enhancements by producing regular status updates
- Report status weekly for all requirements to all stakeholders

Below is the OneERP Demand Management Process for enhancements/demands:

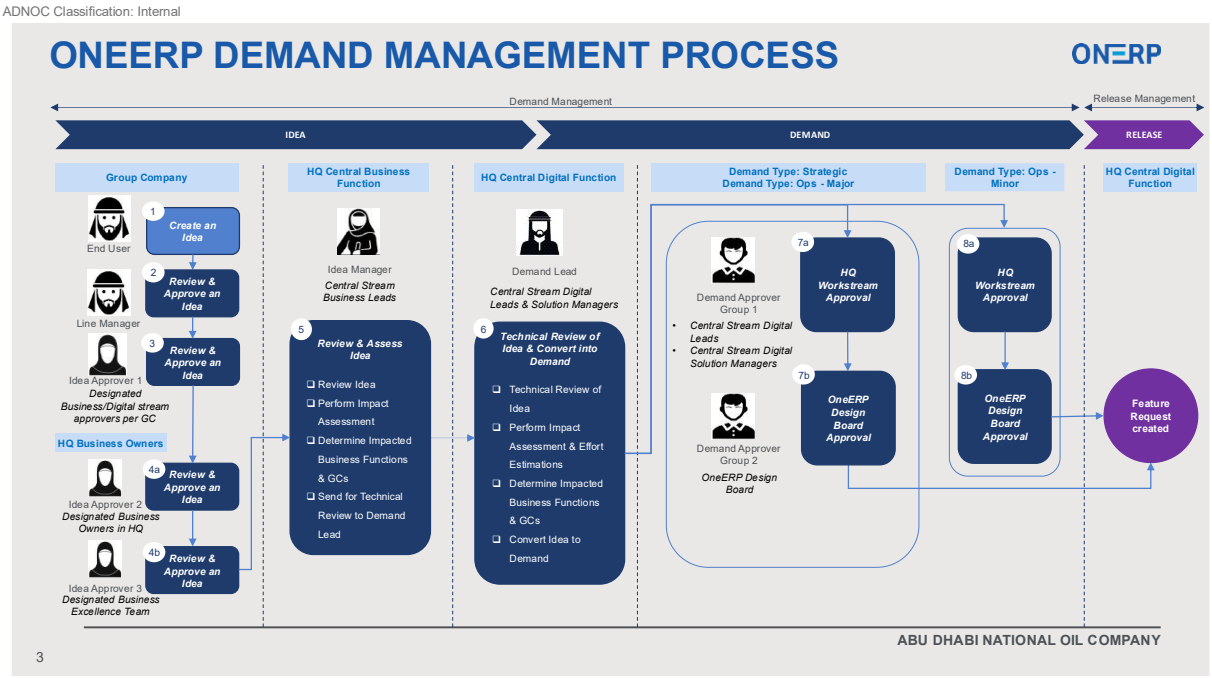

ADNOC Classification: Internal

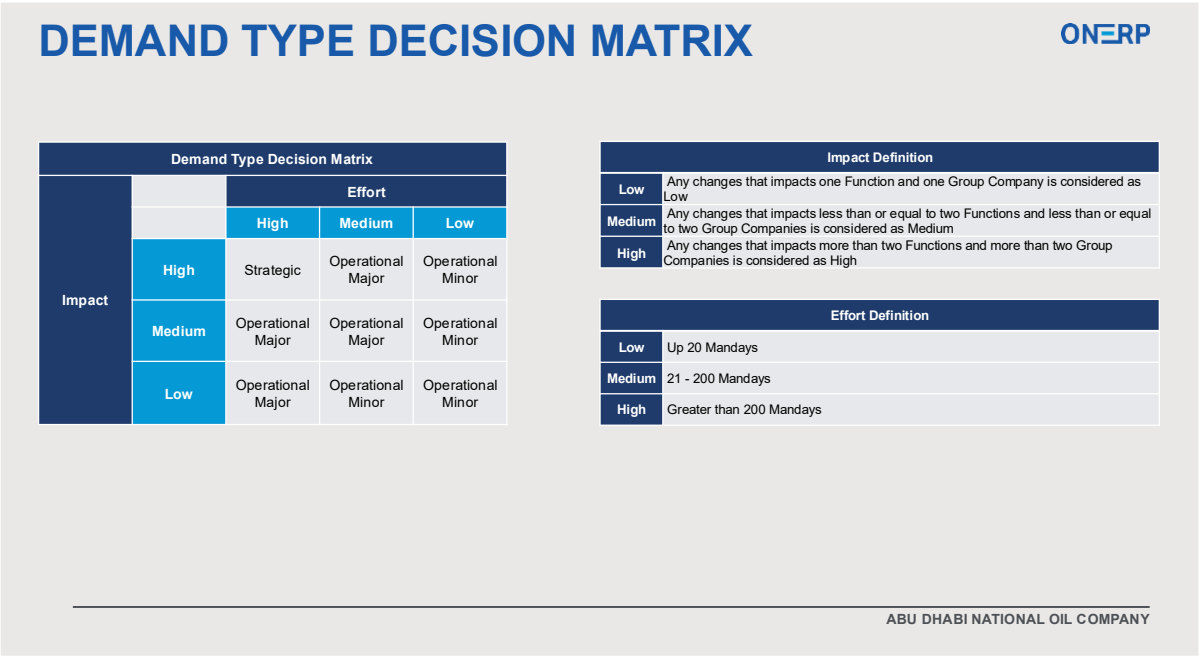

Resource Management processes

ADNOC would like to have the bidder document a clear defined processes to operate and utilize this capacity from the bidder. The following processes need to be detailed in the bid

- Onboarding and Off boarding process of Bidder resources
- Leave Management and absences of resources (Short and long leaves)
- Capacity Planning and Demand Management process to ensure complete utilization of the capacity
- Replacement and Resignation of resources and the Knowledge transfer
    - For any replacement, resignation or long leaves of resources, a minimum of 4 weeks where both resources are working in parallel, and a knowledge transfer is documented will be mandatory. The replacement resource and delivery lead to confirm that the knowledge transfer is received, and new resource is ready to take over.

Project Plan

The Bidder shall provide ADNOC with a project plan that reflects the Bidder's project implementation methodology and provide details of the project lifecycle. The typical plan should include Resource, Roles & Responsibilities, Deliverables, and Activities.

The Bidder shall design the project plan to reflect the following milestones:

- Feasibility Study
- Functional Requirements Collection
- System Design
- System Implementation
- Configuration Verification and Validation
- Acceptance Test
- Acquisition
- Installation
- Maintenance

The Bidder shall provide Project Progress Reporting such as status reports, Weekly and Monthly reports. The deliverables shall meet ADNOC IT PMO standards.

Testing Governance and Processes

For all the line items of scope, the bidder will develop the test strategy that will outline the test phases, cycles, entry and exit criteria, roles & responsibilities and deliverables that will be signed off by key program stakeholders from ADNOC. This might include the proposal of dedicated tooling to maintain the status and outcomes of the differing testing sessions.

- System Integration Testing (SIT):
  - The bidder will prepare the list of test scenarios that will be executed during the SIT phase.
  - The bidder will prepare and publish detailed plan for SIT.
  - SIT test phase is conducted by the bidder and ADNOC may witness the test execution.
- User Acceptance Testing (UAT):
  - The bidder will prepare UAT scenarios and agenda, coordinating with the necessary business stakeholders to conduct the session and record the results and defects in the UAT tracker.
  - The bidder to follow up and prepare remediation plan for the defects found in subsequent UAT cycles.
  - Obtain UAT sign-off from business users.
- Regression Testing:
  - The bidder will utilize/update the existing manual/automated regression test scripts and execute during the Regression Test phase.
  - The bidder will prepare and publish detailed plan for Regression Test.
  - Regression test phase is conducted by the bidder and ADNOC may witness the test execution.

Release Management Plans

All scope items must follow the ADNOC OneERP Governance processes related to Release Management.


Go-live dates must be in line with ADNOC planned release dates. Such release dates will be provided upon award. Proposed work will be executed in the SAP Project Landscape with the following planned cycles and documentation (except for Regression Testing that will be executed in SAP BAU Landscape).

1. Plan
   - Bidder is responsible for providing a plan that details each phase of the deployment cycle to include planned duration and support requirements.
   - Bidder is responsible for presenting and requesting approval from OneERP Design Board for any changes required in OneERP systems
2. Design & Build
   - Bidder will perform Design & Build based on the approved Business Process Document and Design Board approvals
   - Bidder will conduct Unit testing during the Design & Build cycle
3. QA/Test
   - Bidder will conduct Integration Testing during the QA/Test cycle
   - Bidder will provide at minimum 2 data loads to support integration testing and UAT where applicable.
   - Post UAT sign-off from Business stakeholders, Bidder will perform Regression Testing in SAP BAU Landscape
4. Deploy
   - Bidder will follow the CAB (Change Acceptance Board) process and must obtain approval from the board prior to Go Live. The process requires documented plans, approvals, and testing.
   - Bidder is responsible for providing a detailed cutover plan in accordance with ADNOC standards

- Bidder will provide 24/7 support during deployment to Production

5. HyperCare
   - Bidder is responsible for providing HyperCare post deployment
   - Bidder is responsible for proposing a support plan for HyperCare
6. Documentation
   - Project Plan
   - Business Requirements document or Business Process Design
   - Release Management Checklist
   - List of CIs changed/added
   - Installation instructions
   - Maintenance instructions
   - Leasing/Licensing agreements
   - Signed off testing documents (SIT, UAT & Regression Test)
   - Data Migration Plan
   - Installation plans including resources
   - Fall back plans and resources
   - Communication documents
   - User manuals including Technical and/or Functional Design Documents
   - User training plans and education
   - Handover documentation
   - Final acceptance documentation

Below is the OneERP Release management processes for Demands.

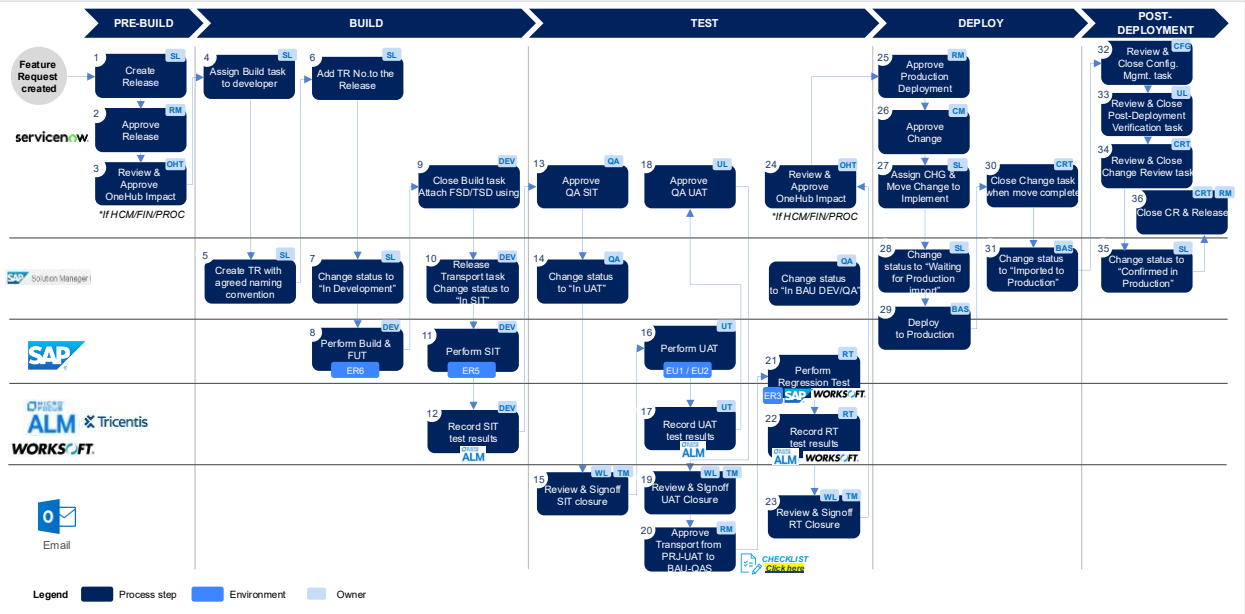

Release Management process for Demands

Below is the OneERP changes Implementation Path & Production transport schedule

Change Type	Implementation Path	Release Class in Service NOW	Frequency	Release Deployment approval to be requested by	Release / Change approval window	Transport movement window	Process/Notes
RITMs (SAP Role Design Change)	Project Landscape > BAU Landscape > Production	Minor	Twice Weekly	2 PM, Monday & Thursday	All changes to be approved by Release Deployment Board and Change Manager between **2:30PM – 3:30PM on Monday & Thursday**	Monday & Thursday, after office hours	• If a release contains both RITM and Incident, it will follow the weekly release window • Only Emergency/Critical Changes (approved by DB) will be allowed to follow "BAU Landscape > Production" implementation path • For critical/off-cycle releases, we will require the approval from VP Group Digital Platforms
RITMs (SAP Role Design Change with cache impact)		Minor	Weekly	2 PM, Thursday	All changes to be approved by Release Deployment Board and Change Manager between **2:30PM – 3:30PM on Thursday**	Thursday, after office hours	
RITMs (Reports - approved in Major/Minor Design Board)		Major/ Minor	Weekly	2 PM, Thursday	All changes to be approved by Release Deployment Board and Change Manager between **2:30PM – 3:30PM on Thursday**	Thursday, after office hours	
Minor RITMs (Feature Request - approved in Minor Design Board)	Project Landscape > BAU Landscape > Production	Minor	Bi-Weekly	Twice Monthly: 8AM, 2nd & 4th Tuesday of the month	**Release Deployment Board:** • **Bi-Weekly Meeting:** 2nd & 4th Tuesday of the month, 9AM – 9:30AM • **Board Members** • **Attendees:** Release requestor(s) and respective Workstream IT Lead(s) • All releases (Minor RITMs) that need to be deployed will be presented in the Release Deployment Board meeting • All supporting data to be attached to associate release and release deployment approval requested in SNOW by Tuesday 8AM • Release Deployment Board will review all releases during the meeting	Subsequent Thursday of Release Deployment Board, after office hours	• If a release contains both RITM and Incident, it will follow the weekly release window • If a release is not submitted for Release Deployment Board by Tuesday 8AM, then it will be considered for the next bi-weekly deployment cycle • Only Emergency/Critical Changes (approved by DB) will be allowed to follow "BAU Landscape > Production" implementation path • For critical/off-cycle releases, we will require exceptional approval from VP Group Digital Platforms
Major RITMs (Feature Request - approved in Major Design Board)		Major	Monthly/ Quarterly	Monthly: 8AM, 2nd Tuesday of the month Quarterly: 8AM, 2nd Tuesday of 2nd month of quarter	**Release Deployment Board:** • **Monthly Meeting:** 2nd Tuesday of the month, 9AM – 9:30AM • **Quarterly Meeting:** 2nd Tuesday of 2nd month of the Quarter, 9AM – 9:30AM • **Board Members:** • **Attendees:** Release requestor(s) and respective Workstream IT Lead(s) • Every month/quarter, all releases (Major RITMs) that need to be deployed will be presented in the Release Deployment Board meeting • All supporting data to be attached to associate release and release deployment approval requested in SNOW by Tuesday 8AM • Release Deployment Board will review all releases during the meeting	Subsequent Thursday of Release Deployment Board, after office hours	• If a release contains both a RITM and Incident, it will follow the weekly release window • If a release is not submitted for Release Deployment Board by Tuesday 8AM, then it will be considered for the following month/quarter • Only Emergency/Critical Changes (approved by DB) will be allowed to follow "BAU Landscape > Production" implementation path • For critical/off-cycle releases, we will require exceptional approval from VP Group Digital Platforms

OneERP changes Implementation Path & Production transport schedule

4.8 Project Location

Project activities are expected to be delivered centrally in one single location, either Adnoc HQ or Adnoc L&S in Abu Dhabi.

User Acceptance Testing, Cutover and Post Go-live first month of Hypercare will be executed in the central location and the two offices of L&S and associated in Singapore and London. Bidder is expected to propose how to split the project staff to cover the activities in these phases across the three locations. The proposal will be inclusive of travel expenses to cover the two additional locations for these specific cases in a fixed price logic.

5 Upgrade Activities

Adnoc ONE ERP is currently on S4H 2109 release and plans to upgrade to S4H 2509 in the 4th quarter of 2026 and 1st quarter of 2027.

Based on past upgrade activities it is expected that the project landscape would have around 2 to 3 weeks of development freeze and 2 to 3 weeks of testing environments downtime.

Bidder has to consider this period in the planning of the 2027 activities.

6 ZMI & Navig8 Reference Architecture

The current detailed architecture landscape for both Navig8 & ZMI is provided as part of the attachments:

- Exhibit 1 - ZMI-Enterprise-Architecture-Landscape
- Exhibit 2 - Navig8-ERP & Business Apps Infrastructure, Integration, and Access Management

7 RFP instruction

5.1 Expected content of the response

Bidders shall submit a comprehensive response including both Technical and Commercial proposals.

Technical proposal

The technical proposal shall include at a minimum

1. A clear solution covering all the Deliverables adequately.
2. For each SOW element, a clear outline of the approach, exemplary deliverables, and best practices. Please label the pages accordingly to indicate which SOW they pertain to
3. A summary of proposed tools and accelerators that will be utilized (e.g., for testing, process design, data cleansing and migration, …)
4. Proposed milestones and timelines of the project in alignment with the overall plan described in this SOW
5. Proposed governance model aligned with the guidelines described in this SOW
6. A summary of the preliminary identified risks, and the suggested mitigation actions
7. Whenever this is relevant a digest of the assumptions used to submit the Proposal. This includes the list of what differs from what has been described in the SOW
8. Company relevant expertise in driving similar transformation across ERP and GBS implementation including reference cases / credentials
9. Company relevant expertise in ADNOC context and in the shipping and marine industry
10. List of CVs of key team members highlighting relevant similar experiences
11. Indicative Mandays estimations (as per the “Exhibit 3 - Indicative Mandays Estimations” template provided) for the core scope line items.

5.2 Evaluation Approach

ADNOC Digital & L&S will evaluate the Technical Proposal based on the defined approach below. The technical evaluation will consider, among others, the following aspects:

- Alignment of the proposed timeline with ADNOC L&S program plan
- Robustness of the delivery approach, including methodology, tools, and assets across the different components of the SOW
- Demonstrated experience in delivering similar transformation programs
- Experience within ADNOC and familiarity with its systems, governance, and operating environment
- Industry knowledge and relevant sector experience
- Strength and suitability of the proposed team, including the quality and relevance of submitted CVs

- Understanding of the 3 strategic streams, their integration logic, dependencies and constraints: Bidder to demonstrate a clear understanding of the engagement as one integrated transformation spanning: (i) ERP implementation, (ii) GBS design, and (iii) infrastructure alignment. The response should explicitly describe how the 3 streams influence each other, what key decisions sit on the critical path, and what dependencies, constraints and sequencing considerations must be managed across ADNOC L&S, ZMI and Navig8.
- ERP business transformation and fit-to-gap solution approach: Bidder to demonstrate the understanding of the ERP stream across enterprise structure, fit-to-gap process design, localization across ADNOC L&S / ZMI / Navig8, integration-led redesign and the role of SAP as the backbone for enterprise processes, and business applications for day to day business operation. The response should demonstrate how the bidder will translate the current fragmented landscape into a controlled future-state model aligned to OneERP standards.
- Transformation vision, business outcomes and user value proposition: Bidder to present the transformation vision and business outcomes for ADNOC L&S, ZMI and Navig8, including what will materially improve for leadership, business users, support teams, approvers and other stakeholder groups. Strong responses should move beyond a system implementation narrative and explain the practical benefits, business outcomes and “what’s in it for me” for the people impacted by the change. Bidder to address the user journey across design, testing, training, go-live and hypercare. The response should explain how impacted users will experience the change, how resistance and adoption risks will be managed, how training and digital guidance will be tailored, and how the bidder will help users transition into the future state confidently and sustainably.
- GBS design approach, implementation realism, and ERP-aligned transition: Bidder to demonstrate the understanding of the GBS stream across both design and implementation dimensions, including their proposed approach to defining the future Finance and Procurement service model and their ability to practically transition and embed it alongside the ERP rollout. The response should address service scope, service catalogue, SLA/OLA framework, target model options, retained organization, governance, sourcing/location considerations, and transition roadmap, while clearly demonstrating how process standardization, retained roles, business ownership, and service performance management will be aligned to enable a phased transition from current entity structures to the target model and deliver measurable business value beyond centralization.
- Integration ecosystem, RICEFW, enterprise enablement and practical delivery assets: Bidder to demonstrate the practical enablement approach that supports the three streams, including integration architecture, third-party collaboration, RICEFW governance, and automation across systems such as IMOS, EyeShare, Ship Management Solution, DigitALL Ocean, BOS, Ariba, ILMS, SmartPort, payroll interfaces, SAC and SuccessFactors and enterprise data considerations, traceability, assumptions, tools & accelerators. The focus is on whether the bidder’s proposed solution is implementation-ready and supported by practical enablers rather than being only conceptual.
